




PROJECT MANAGEMENT

IMVANO RESOURCE CENTER - IREC.

LESSON 2

START THE PROJECT

- Identify and Engage Stakeholders
- Form the Team
- Build Shared Understanding
- Determine Project Approach

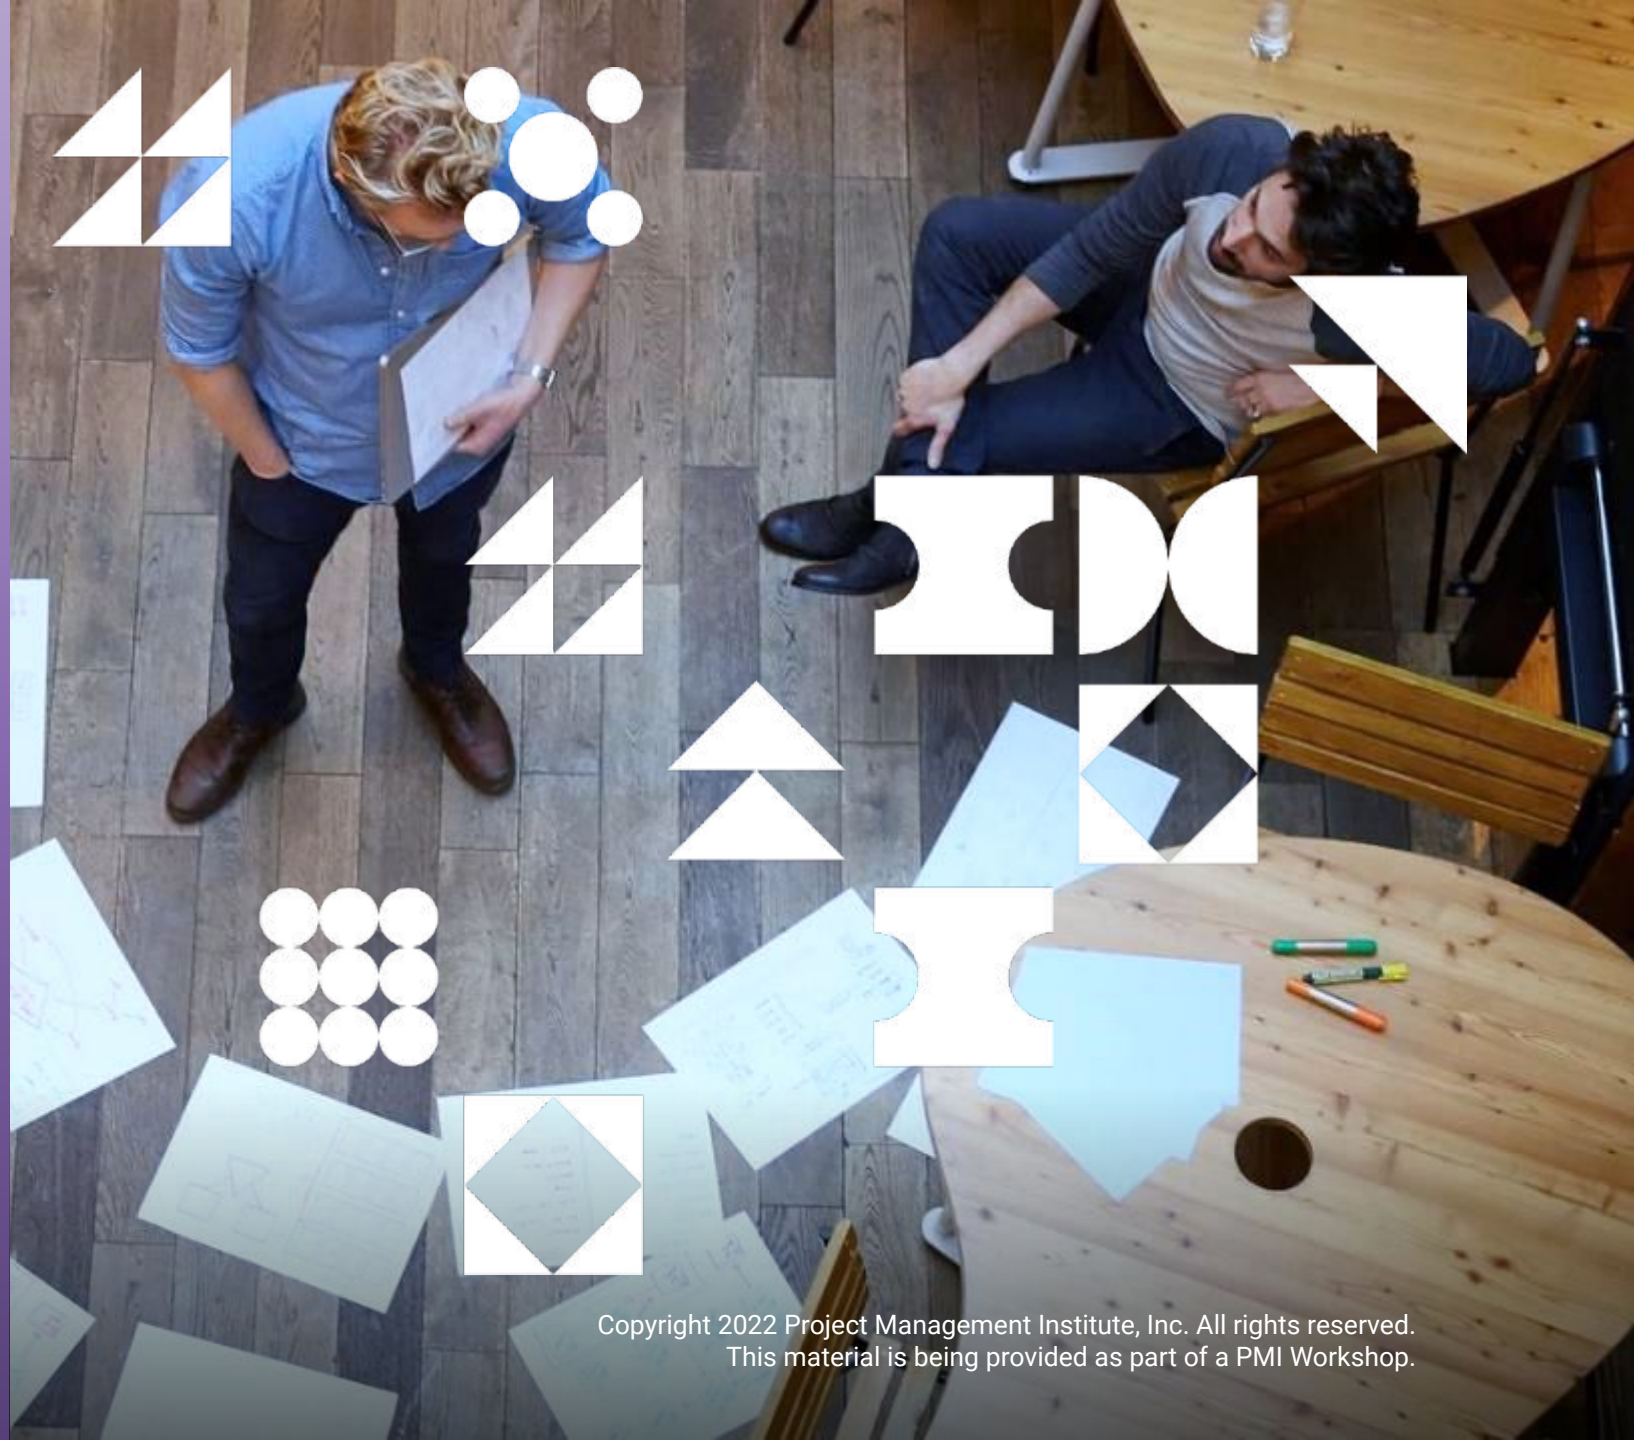

Learning Objectives

- Define and discuss stakeholders and the most effective ways to communicate with them.
- Explain the best ways to form a team.
- Describe how to build the most effective understanding of a project and how doing so relates to executing a project successfully.
- Explain how predictive and adaptive project life cycles work; explain what a hybrid development approach is.
 - Decide which kind of development approach or life cycle is best suited for work.



Identify and Engage Stakeholders

TOPIC A

Lesson 2

Outline

- **Definition of project stakeholders** – Individuals, groups and organizations who may affect, be affected or just perceive that they may be affected.
- **Stakeholder Identification** – Identify internal and external stakeholders of a project as early as possible – typically during project charter development.
- **How to identify stakeholders** – carry out document review, data gathering, brainstorming, review past project files etc.
- **Stakeholder Register** – Captures and records important stakeholder information. It is updated continuously.
- **Stakeholder analysis** – using an onion diagram, power/interest, power/influence, salience model (power, urgency and legitimacy), stakeholder cube (power, interest and attitude).
- **Stakeholder engagement assessment matrix** – identifying stakeholders as unaware, resistant, neutral, supportive and leading.
- **Stakeholder engagement plan** – identifies required management strategies to effectively engage stakeholders.
- Communication requirements analysis.
- **Communication model** – Sender/Receiver mode and the potential noise.

Stakeholder



DEFINITION

An individual, group, or organization that may affect, be affected by, or perceive itself to be affected by a decision, activity, or outcome of a project, programs, or portfolio.

Know Your Project Stakeholders!



Typical Project Stakeholders*



Can you categorize these stakeholders?

- *Which are typically project team members? Which are not?*
- *Which are typically active in project work?*

Identify internal and external stakeholders of a project as early as possible — typically during project charter development.

For example, this is a visualization of the kinds of roles and people who can be project stakeholders.

Stakeholders:

- Take on a variety of roles and responsibilities on a project.
- Can include members of the project team, customers, end users, business or project partners, and others.
- May or may not be actively involved in project work.
- Could affect or be affected by a decision, an activity or an outcome of a project.

Typical stakeholders may include:

- ***End users; Customers; Employees; Organization; Managers; Sponsors; Business partners; Suppliers and contractors; Government; Community.***



Project Stakeholder Management.

- **Every project has stakeholders who are impacted by or can impact the project in a positive or negative way.**
- Some stakeholders may have limited ability to influence the project's work or outcomes; others may have a significant effect on the project or its outcomes.
- **The ability of the project manager and the team to correctly identify and engage all stakeholders in an appropriate way can mean the difference between project success and failure.**


Create and maintain relationships between the project team and stakeholders.



Stakeholder and Communications Management Overview

- Stakeholder register
- Stakeholder engagement plan
- Communications management plan
- Stakeholder engagement assessment matrix (SEAM)
- Assessment grids / matrices / models.

You will develop and update this set of project artifacts together, and they will, of course, be tailored to your project and updated as necessary.

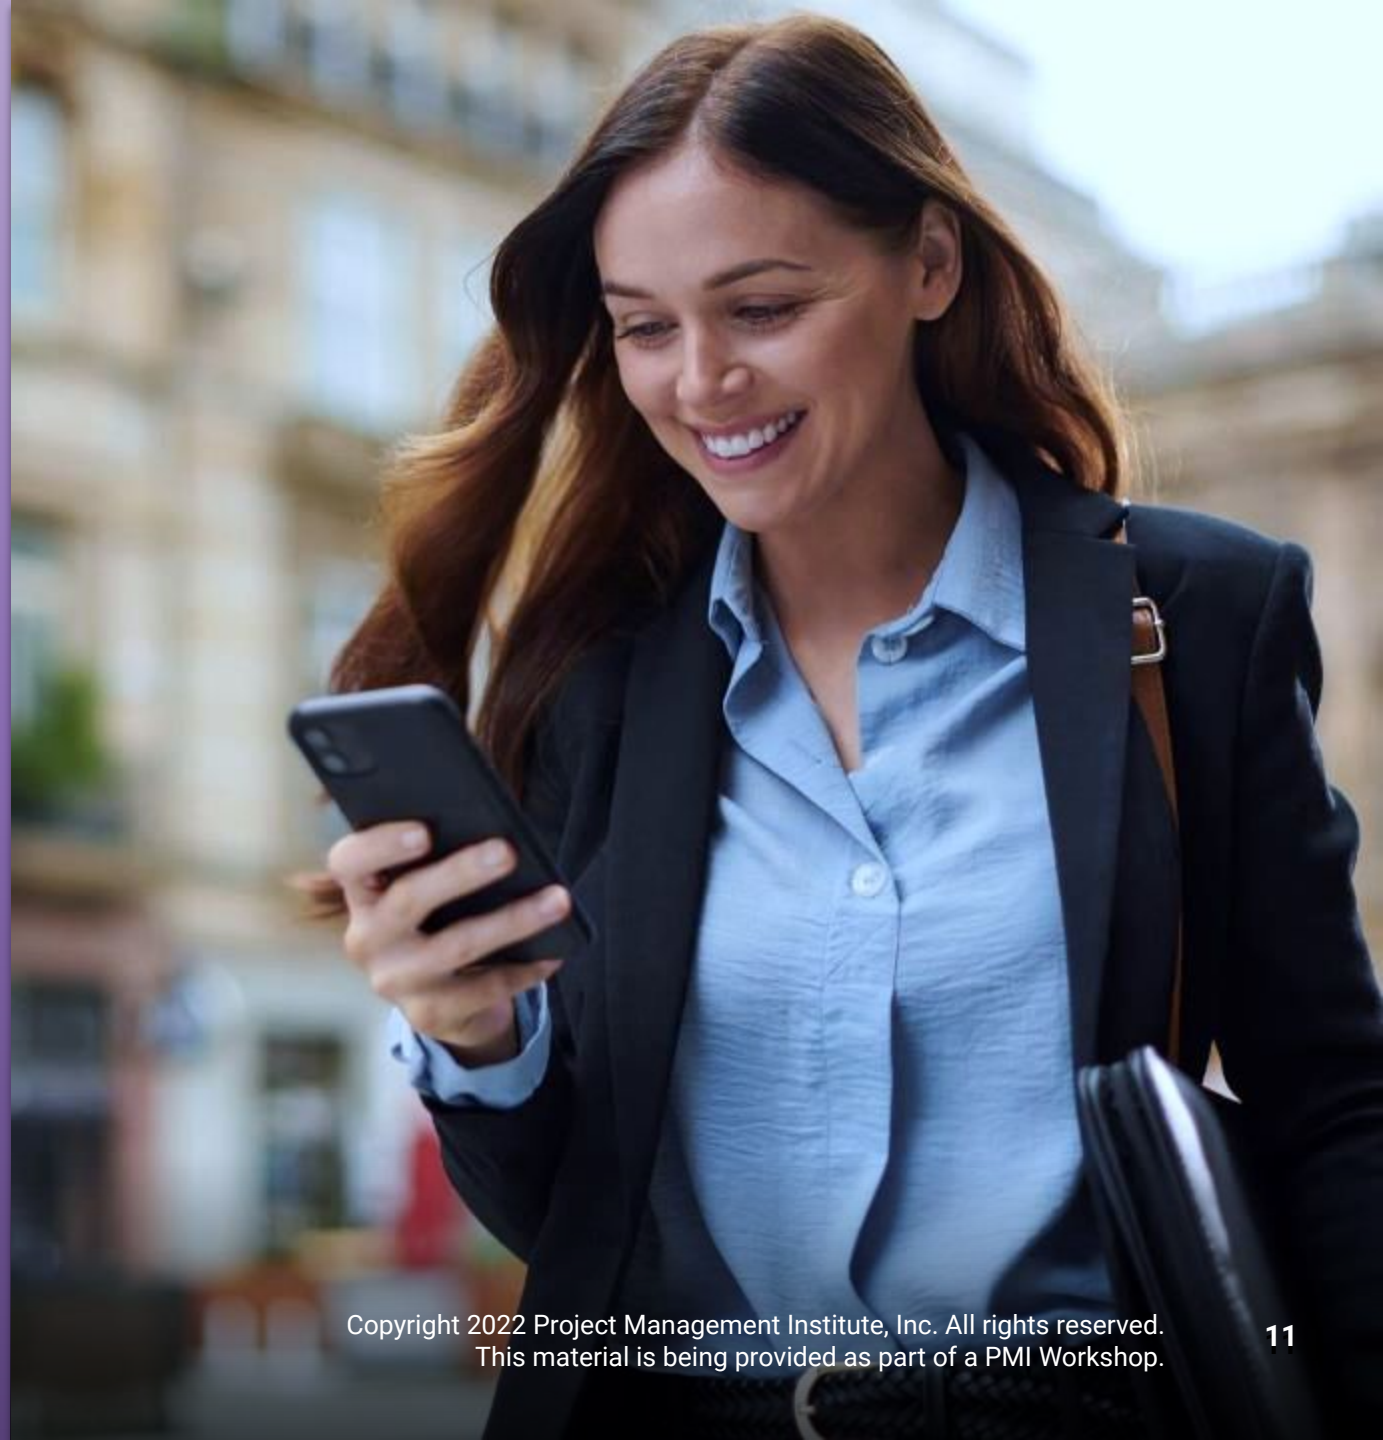

Stakeholder Identification.

- **For smaller projects**, you can be very thorough in your identification and assessment of stakeholders and in developing an effective communications strategy with your stakeholders.
- **For larger projects**, or those with a challenging stakeholder environment, you should also try to be as thorough as possible, focusing on key stakeholders and groups. In those cases, the power/influence/impact grids and salience model tools will be more helpful to you.



Identify and engage stakeholders early to avoid surprises later in the project!

Stakeholder Identification

Who are they?

- Check the **business case** and **benefits management plan** for names
- Later, check the **issue/impediments log**, **change log** or **requirements documents** to see who else is needed or named

What's their relationship to the project?

- Interest
- Involvement
- Interdependencies
- Influence
- Potential impact on project success

Assess Stakeholders.

STAKEHOLDER ANALYSIS

A technique of systematically gathering and analyzing quantitative and qualitative information to determine whose interests should be considered throughout the project.

Data Gathering

- Questionnaires and surveys
- Brainstorming

Data Analysis

- **Stakeholder analysis** — What are their “stakes” in the project? — i.e., interest, rights, ownership, knowledge, contribution
- Document analysis

Data Representation

- Two-dimensional (2D) grids
 - Power/interest
 - Power/influence
 - Impact/influence
- 3D grid — Stakeholder “cube”
- Salience model
- Directions of influence

Create the Stakeholder Register.

STAKEHOLDER REGISTER

A project document including the identification, assessment, and classification of project stakeholders.

- Capture and record important stakeholder information.
- Factor in OPAs.
- Update it! Describe the evolving relationship with stakeholders throughout the project.



Contains the information necessary to execute the stakeholder engagement plan.



- Refer to **stakeholder registers** from previous, similar projects for help
- Remember this is a public document, so ensure the information presented is appropriate

Stakeholder Register.



	Name	Title	Internal / External	Project Role	Major Requirements	Expectations	Influence / Attitude
1	Eugene Lowe	CEO	Internal	Sponsor	Successful completion	On-time completion, successful partnerships	Champion
2	Oasestown Municipality		External	Government partner (liaison); funding contributor; owner of SLC site	Successful completion of facility and partnership;	Accountability	Supporter
3	Kara Black	Principal, Oases Architects	External	Partner, designer, specialist knowledge (conservation building)	Clear design brief, successful partnership	Fluid funding and communication, design autonomy	Champion
4	Josie Bynoe	Chair, BOD	Internal	Direct strategic local partnerships for Shawpe	Environmental sustainability of project work; "moral rights"	No damage to Oasestown conservation district or environs	Resistor
5	Helen Grey	Lead, business development	Internal	Product owner	High profile tenants, excellent community and conservation credentials	Organizational learning; leadership opportunity	Neutral
6	Hasan Persaud	VP of Business Development	Internal	Portfolio owner	Capacity for ongoing revenue	End-user in Phase 3	Neutral
7	Mandeep Chahal	VP of Finance	Internal	Budget controller	direct contact with funding partners	clear data	Neutral
8	Kei Leung	VP of Marketing	Internal	Marketing expert	elevation of brand	high quality tenants	Supporter
9	Tenants		External	Income source	bespoke spaces	high quality	Neutral
10	Contractors		External	Vendors - building	clear instructions, contract		Neutral
11	Oasestown local residents		External	Neighbors to project	Traffic and noise pollution management	no inconveniences	Resistor
12	Oasestown Community Partnership		External	Community group operating in Oasestown	none	a free space in the SLC	Champion

Sample.

Stakeholder Register

Stakeholder Name	Contact information	Project Role	Project Requirements	Project Concerns	Impact and Influence Scores
Mary Pulaski	(123) 1234567 mpulaski@hmail.com	Sponsor	Compelling UI, fast and responsive	Delays, cost over runs, poor reacti	●●● ■ ■ ■
Libby Kipling	(123) 2345678 lkippling@hmail.com	Project Manager	Completion to scope, schedule, budget & q	Tech viability, Disappointed Sp	●●● ■ ■ □
Jeff Harris	(123) 3456789 jharris@hmail.com	Product Manager	Fully functional app with all high priority	Ready for trade show, slower tha	●●● ■ ■ ■
Mitchel O'Keath	(123) 4567890 mokeath@hmail.com	PMO Representative	Alignment with IS strategy, integration	Citizen dev. risks, dependencies on	●○○ ■ □ □
Sanjiv Patel	(123) 5678901 sapatel@hmail.com	Steering Committee Mbr	Competitive advantage, ROI	Industry reception, costs	●○○ ■ ■ ■
Joe Corbitt	(123) 6789012 cuttiepie@hmail.com	Development Team Member	Delight the users, gain team lead exper	Team skills, lack of Xcor experien	●●○ ■ □ □

Stakeholder Register



Profile information:

- **Name or organization:** Stakeholders can be individuals or entities.
- **Title:** Their functional position in the organization or elsewhere.
- **Project Role:** Position on the project.
- **Major Requirements:** Which of the project requirements stakeholders are concerned with?
- **Internal/External:** Is their role inside the company or not?
- **Communication type:** What is their preferred method/frequency of communication?

Assessment information:

- **Expectations:** Take note of their expectations of the project. You will have learned this during an interview, for example.
- **Influence:** What degree of impact can this stakeholder have on the project? Use descriptive terms and ensure everyone understands what the terms mean.

Directions of Influence.



You should **understand the social network of project stakeholders**, specifically the direction of their influence on the project.



Upward	<i>Parent organization</i> — senior management (business, financial interests)
Downward	<i>In the project hierarchy</i> — team or specialists
Outward	<i>Have a “stake” in the project</i> — client, end-user, external
Sideward	<i>Friendly or competitive for resources</i> — project manager's peers, other organizational departments

Know Your Stakeholders

Go Beyond Job Titles

Power	Level of authority
Interest	Level of concern about project outcomes
Influence aka attitude or impact	• Ability to influence project outcomes or cause changes to planning or execution • Magnitude of potential contribution or disruption to project <i>Use a descriptive term – e.g., champion, supporter, neutral, detractor</i>





Tailor stakeholder assessments to suit project needs. The goal of this exercise is to facilitate your planning of effective communication with the stakeholders!

Stakeholder Mapping

Use two dimensions to map stakeholders:

- **Power** and **interest** grid
- **Power** and **influence** grid
- **Impact** and **influence** grid

Or use three dimensions – a **cube** – to refine the analysis further!

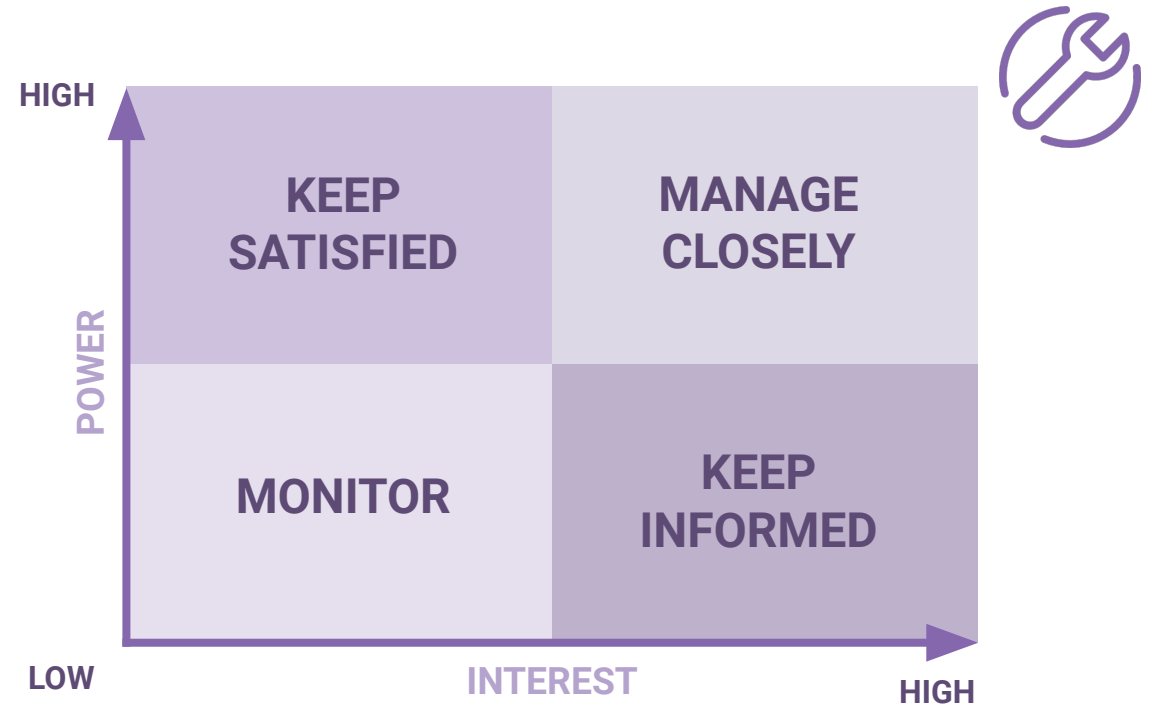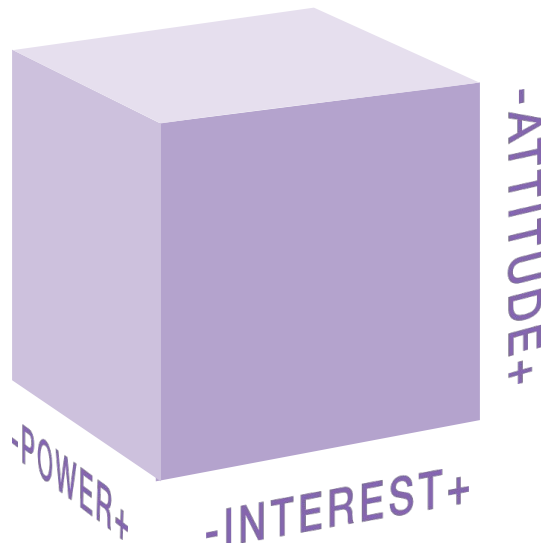

Method:

- Place each stakeholder on the grid
- Use the same quadrant labels, but change the axis labels

Stakeholder Mapping



Method: Power and interest grid/Use two dimensions to map stakeholders:

- Place each stakeholder on the grid



Stakeholder Mapping.




2D Models: Power/interest grid. The four quadrants on the matrix:

- **High power – High interest:** Who are the people that we should actively engage with? Who are the decision makers that have the biggest impact on the project?
- **High power – Low Interest:** Who should we actively consult? Who are the people with great power, but with little time to dedicate to the project?
- **Low power – High interest:** Who should we invite and maintain a close relationship with? Who are the people most interested in the project, but that have low power?
- **Low power – Low interest:** Who should we keep informed? Although we will not spend time and energy with excessive communication.



- **3D Model: Stakeholder Cube.** This is a refinement of the 2D grid models that combines grid elements into a three-dimensional model that can be useful with the development of communication strategies.
- Map dimensions of **power, influence, impact or attitude** toward the project. *See next slide.*

Stakeholder Cube

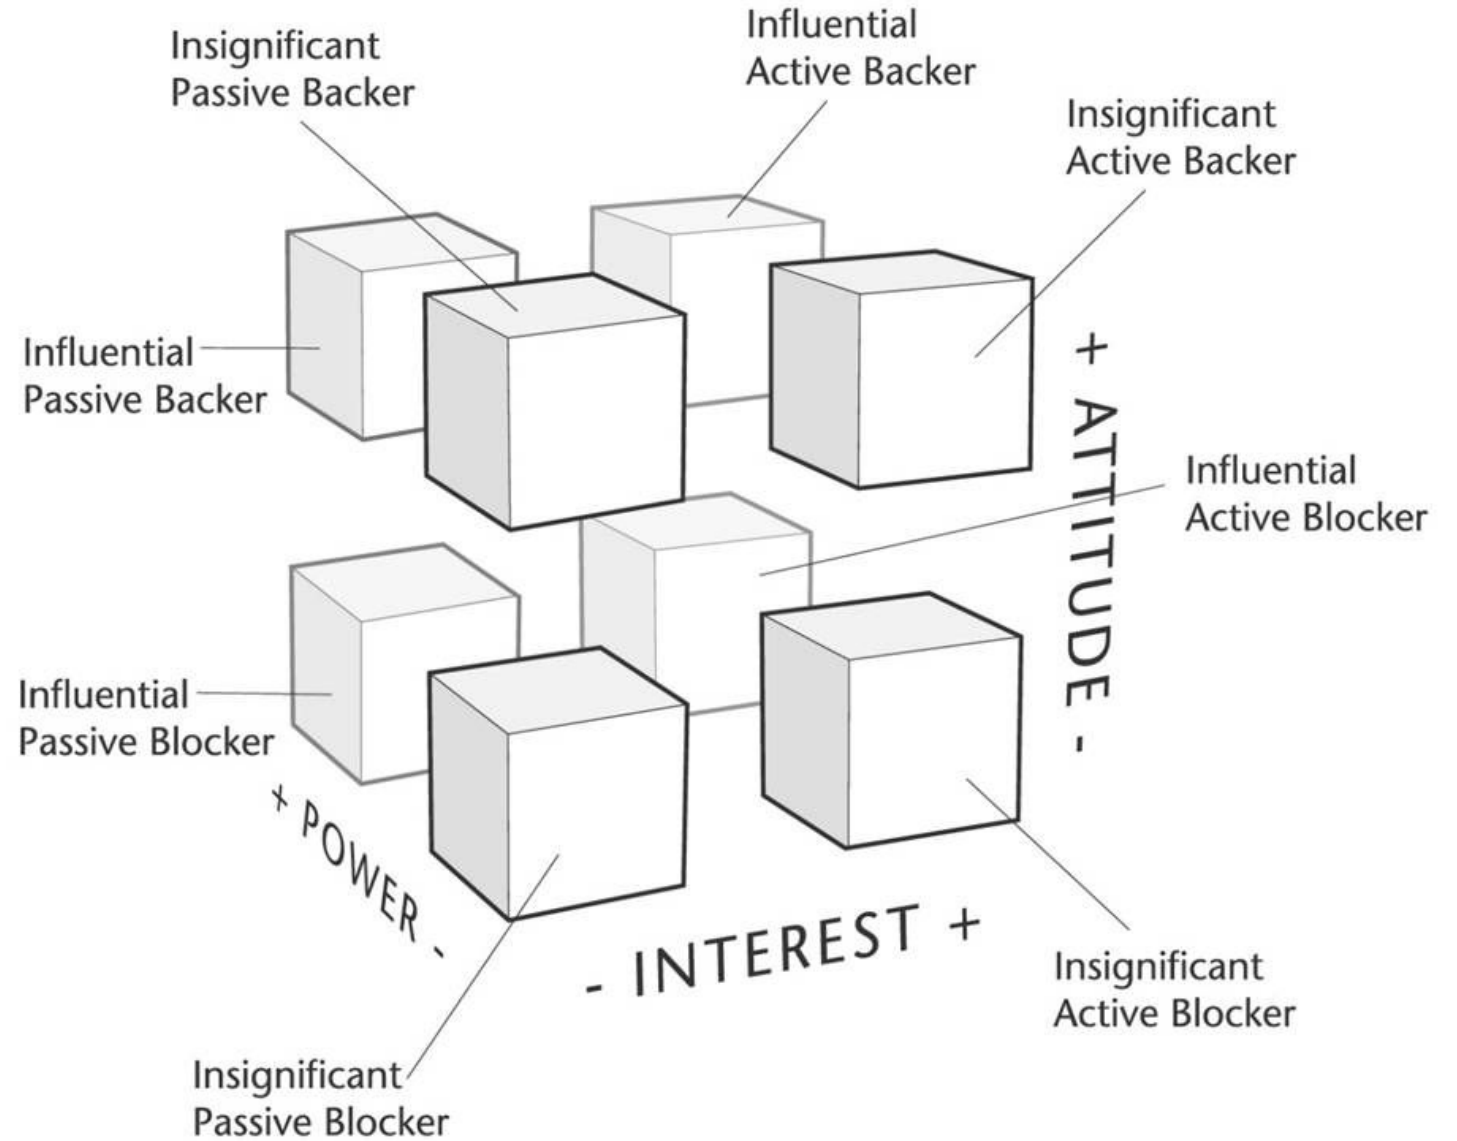

Salience Model



Focus on the **product owner** role. Are they familiar, interested and engaged enough with the project to make decisions and move the project forward?


The **salience model** is another way to assess stakeholders based on their:

- Level of authority (**power**);
- Immediate needs (**urgency**);
- and how appropriate their involvement is in terms of the project (**legitimacy**).

*This is especially important for the role of **product owner**:*


- *Do they understand the current situation?*
- *Can they help move the project forward toward the vision?*
- *Can they make decisions when changes are required?*

Salience Model

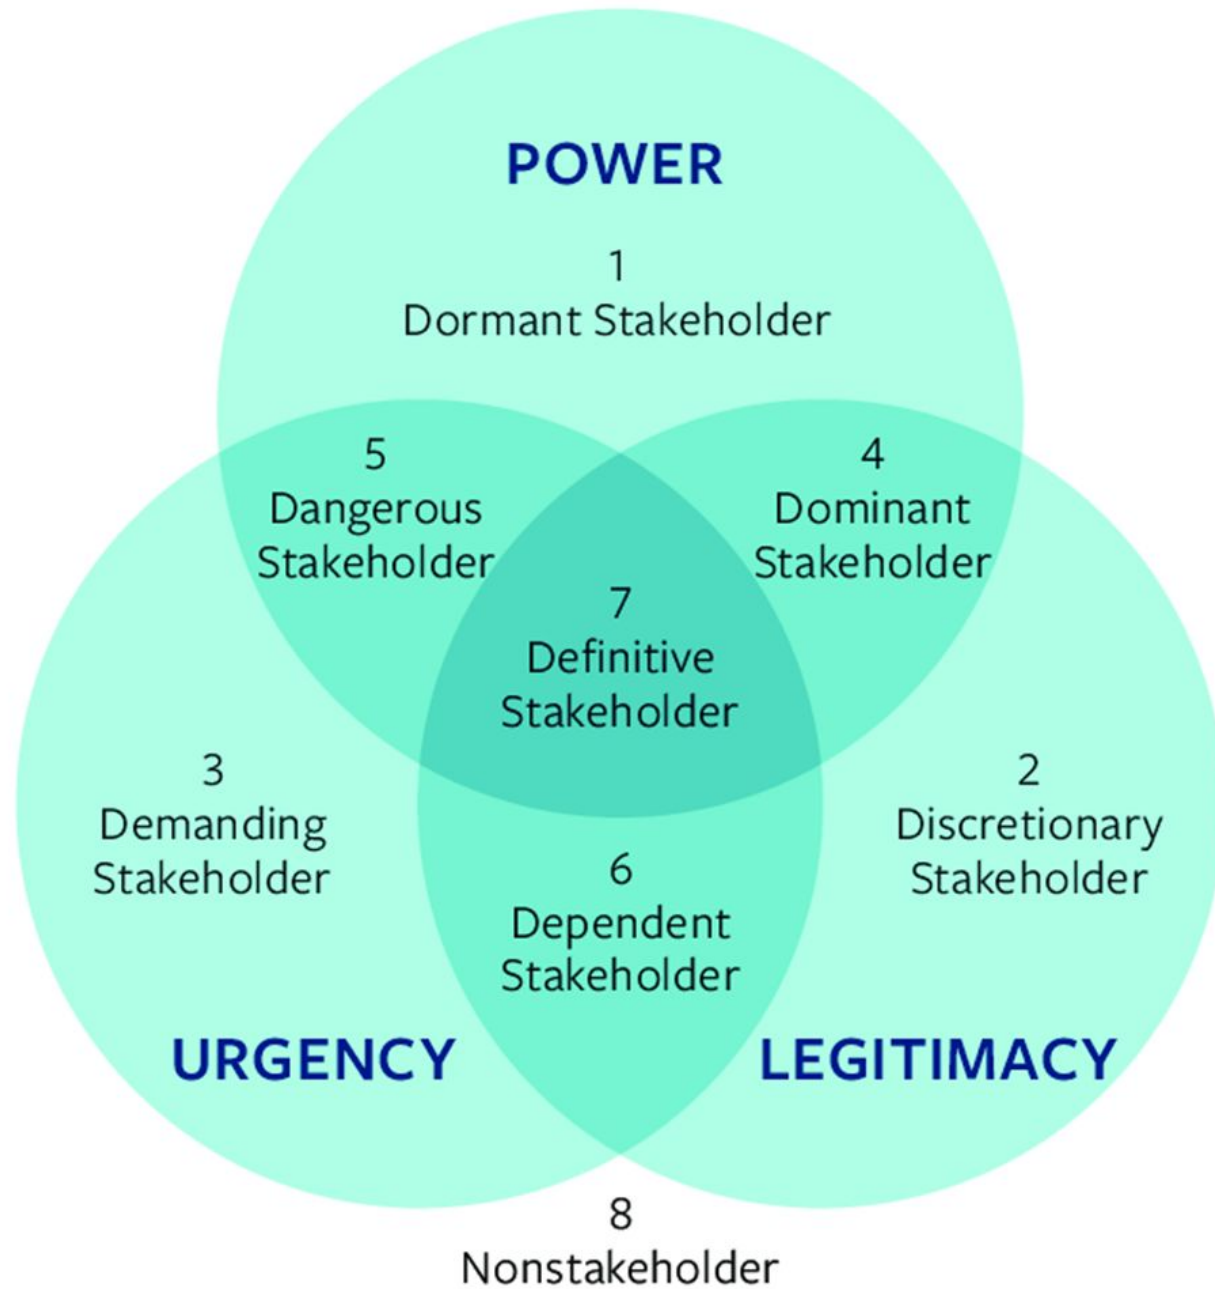

Stakeholder Analysis - Onion diagram.

The Stakeholder Onion Diagram shows your stakeholders on a chart, with the inner circle consisting of your key stakeholders who are closest to your objectives and issues. The next circle outward is considered to be primary stakeholders, and your outer circle shows secondary stakeholders.

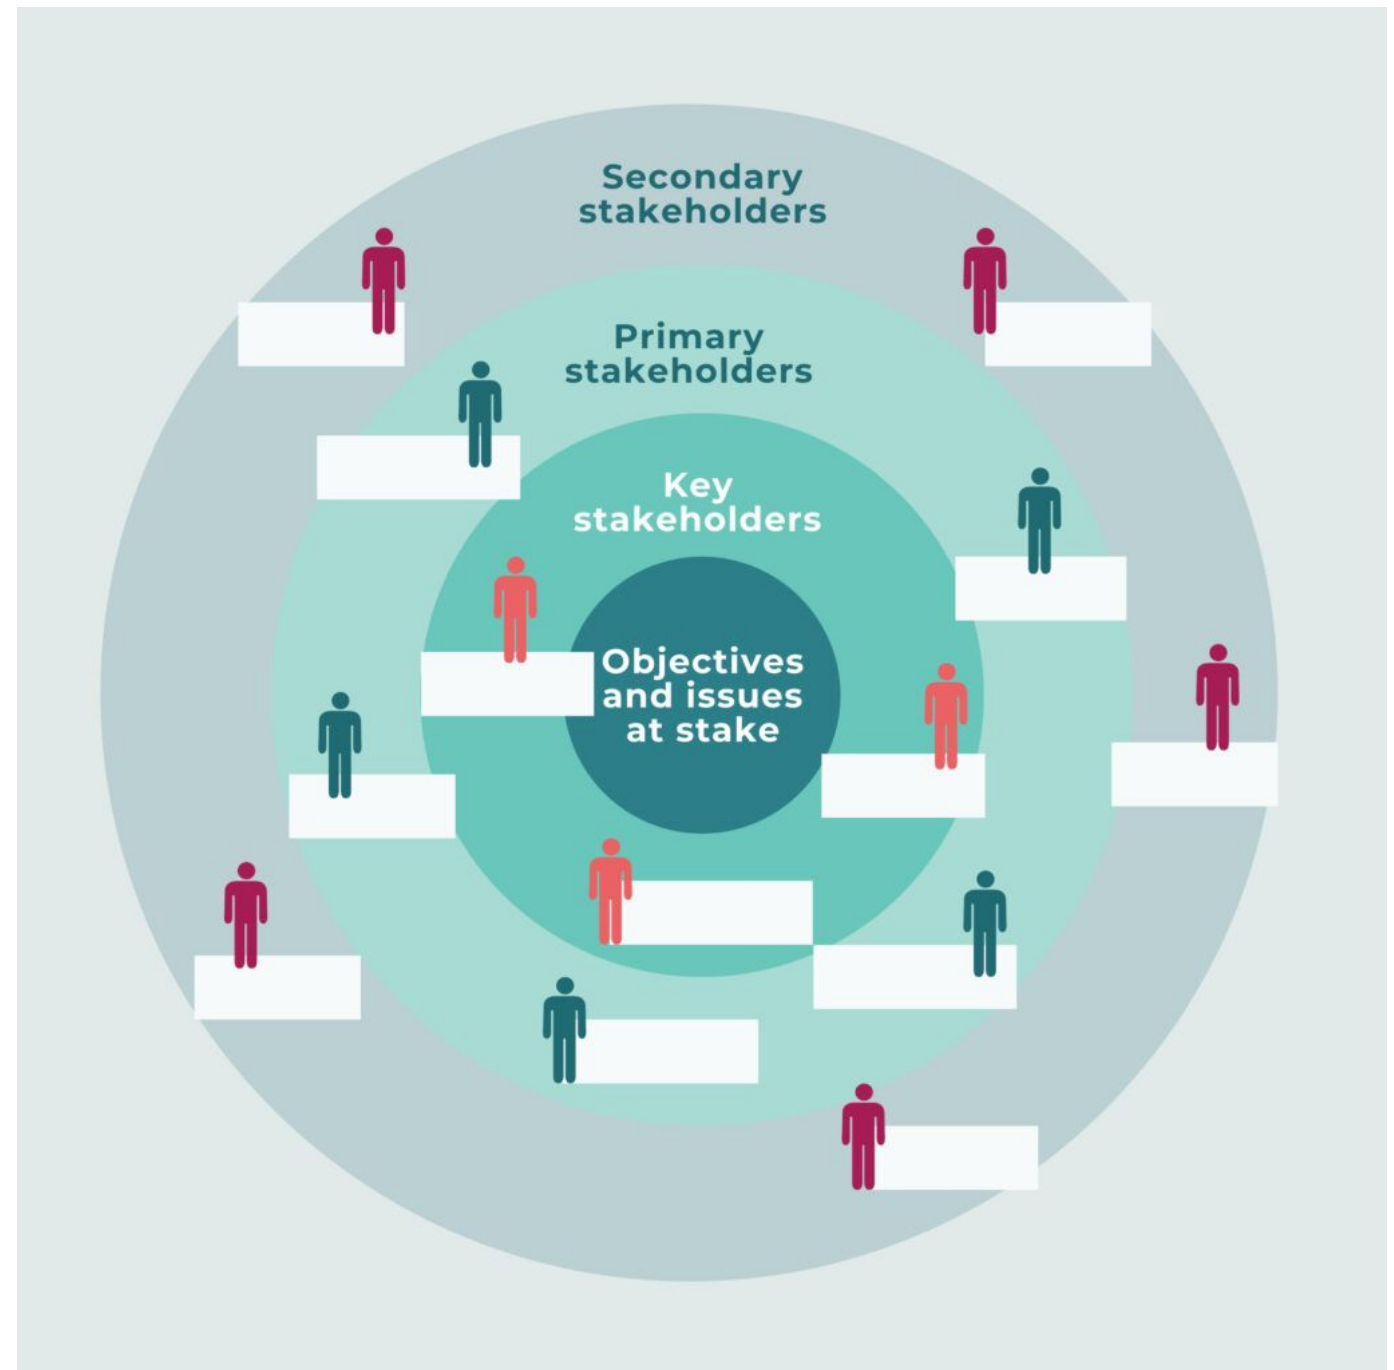

Stakeholder Engagement Assessment Matrix.



DEFINITION

A matrix that compares current and desired stakeholder engagement levels.

Stakeholder Engagement Assessment Matrix – SEAM



- The final piece to create before planning and getting to work is the **stakeholder engagement assessment matrix (SEAM)**. This information will be very useful to know at various moments of the project.
- Create a grid listing all the stakeholders and **note their current level of engagement, then indicate the “desired” level of engagement**. Immediately, you will see how much **work you must do to convert the status of each stakeholder to “desired”** and it sets the stage for your planning.
- *Tailor labels for stakeholder levels of engagement to your context, team or organization.*
- **Enables easy tracking of stakeholder engagement levels during the project.**

Project Stakeholder Classification

- Analysis of stakeholders informs the project managers, which stakeholders are:
 1. Unaware.
 2. Resistant.
 3. Neutral.
 4. Supportive.
 5. Leading.
- Stakeholders can be an asset or a problem on the project, depending on how well the project is planned.

Stakeholder Engagement Assessment Matrix.

Stakeholder	Power/ Influence	Unaware	Resistant	Neutral	Supportive	Leading
Sponsor	H/H				C	D
Manager	H/H			C	D	D*
Legal	H/L	C		D		
Low Impact	L/L	C		D		
Staff	L/H		C		D	D*
C = Current level of engagement D = Minimal desired level of engagement D* = Optimal desired level of engagement						

Stakeholder Perceptions

- Must be holistically understood in customer-centric project management approaches .
- Can be damaging to a project, whether they are negative or positive.



Why do you think it's important to understand both positive and negative stakeholder perceptions of your project?



Capture Stakeholder Feedback and Perceptions



- *Interpersonal skills*
- *Active listening*
- *Emotional intelligence*
- *Effective communication methods*



Key stakeholders

- Interview to understand **project requirements and vision** and **communication preferences**



All stakeholders


- Appropriate, regular project communications



Large and public groups

- Questionnaires/surveys
- Facilitated conversations/sessions — online or in person
- Digital media – email campaigns, websites, group chats
- Posters and advertising

Plan to Communicate with Stakeholders



- **Stakeholder engagement plan** identifies the required strategies and actions required to promote productive involvement of stakeholders in project decision-making and execution. Used to understand stakeholder communication requirements and the level of stakeholder engagement.
- Team fulfills strategies via communications described in the **communications management plan**.
- The stakeholder engagement plan and the communications management plan are interlinked artifacts.
- **Using the information in the stakeholder register and doing some further analysis, you create the stakeholder engagement plan and the communications management plan.**

Communication Requirements Analysis

- Leads to a clear **articulation of the stakeholders' communications needs.**
- Enables effective choices about **communication topics, frequency, models and technologies.**
- Output is a grid, questionnaire or survey that documents the communication and technology requirements for each stakeholder



Communication: Methods and Technologies



Communication: Methods and Technologies



Do you use any other communication methods or techniques on your projects?

Are there types your organization does not allow? Why?

Meetings/verbal

- Physical (face to face)
- Virtual (videoconferencing)
- Phone call

Digital/electronic media

- Websites and social media
- Instant/text messaging via phone or platform
- Email or fax

Physical

- Body language and gestures
- White boards


Communication: Methods and Technologies

- You need to ask stakeholders directly about their **communication requirements**.
- Doing so leads to a clear articulation of the stakeholders' communication needs.
- Think of the diversity of communication methods available for use on projects.
- **With technology factored in, you need to think about suitability of use in addition to security and encryption matters for communication of project work.**

Idea: Can you think of other ways we communicate on projects?
Some professions use unique communication technologies – for example, faxes in the medical and legal professions.



Communication Methods



Push — sender determines:

- Send an email
- Make a phone call


Pull — receiver determines:

- Post information on team board
- Store reference documents in electronic repository — e.g., SharePoint



Interactive communication is a method which enables both sender and receiver to interact in real or near-real time.

- Conversation (virtual or in person)
- Workshops/collaboration
- Whiteboarding



Agile teams are colocated whenever possible so that they can be highly collaborative.

Communication Challenges / Considerations



You should consider the following challenges when determining the method and frequency of communications.


- Urgency of need for information
- Availability and reliability of technology
- Ease of use
- Project environment – e.g., language and formality
- Sensitivity and confidentiality of information
- Communications OPAs – e.g., social media protocols
- Data protection laws/regulations
- Accessibility requirements.

Communication Model*



Think of an example of a transmission. Depending on the method, what kinds of noise can play a part?

Cross-Cultural Communication Model: A description, analogy, or schematic used to represent how the communication process will be performed for the project.

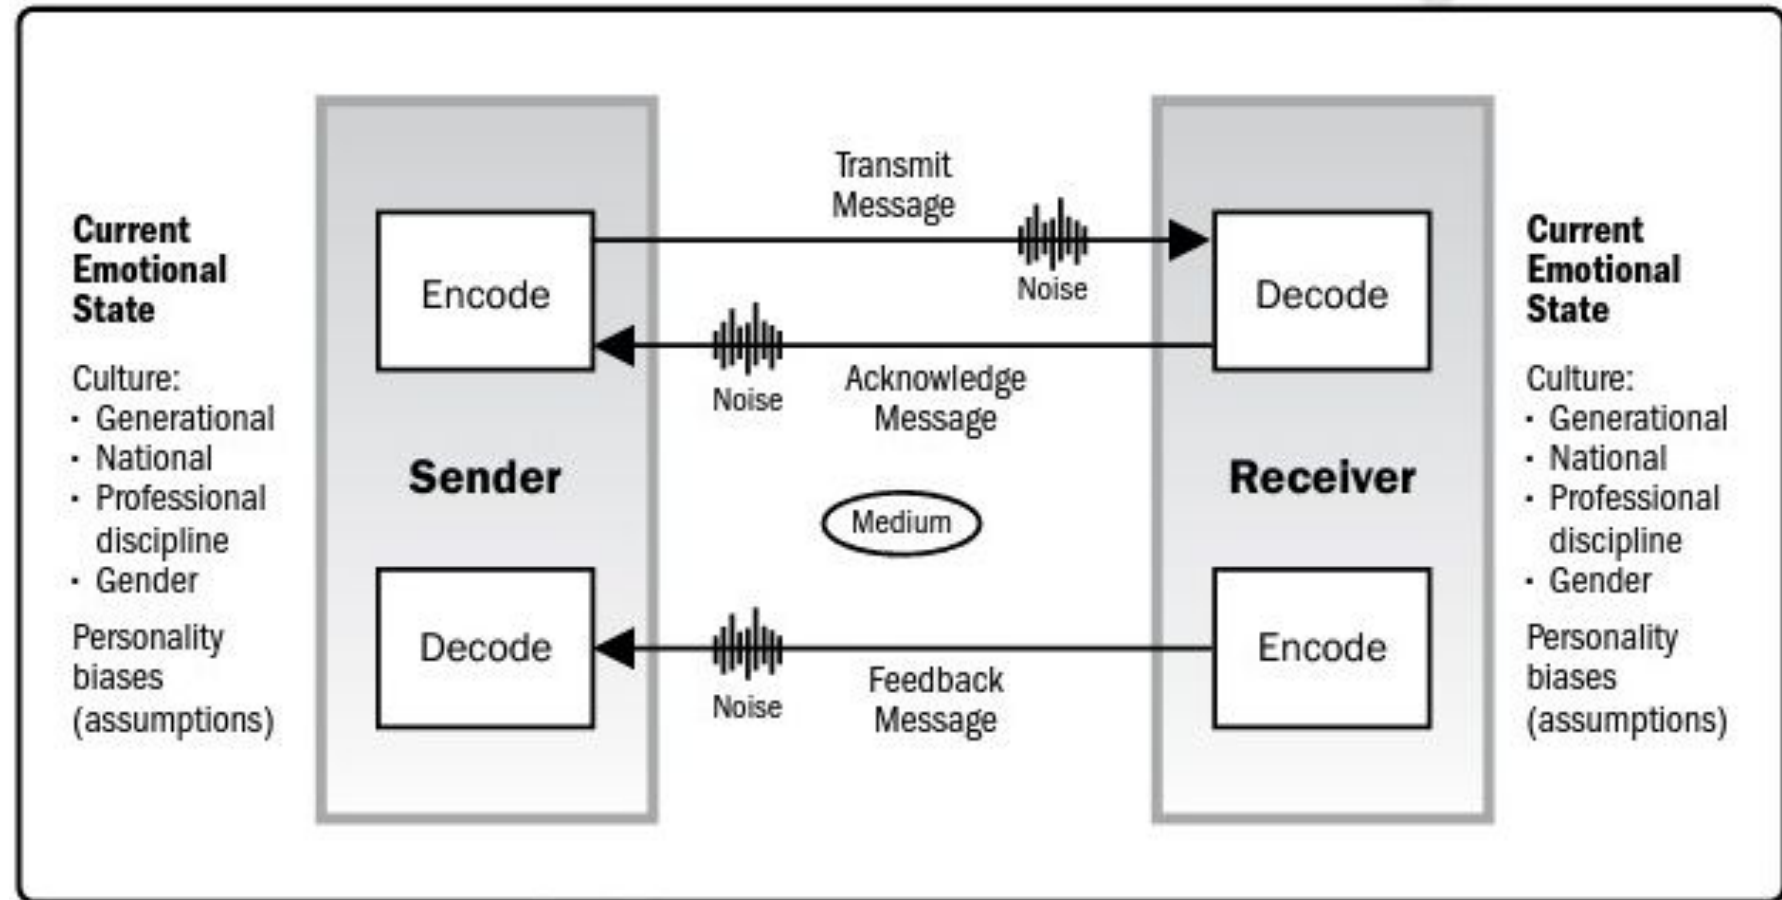

Noise in communication.

Are we communicating?



DEFINITION

NOISE

- Any interference in the communication process that prevents the message from being heard correctly, and it can occur at any point in the process
- ***External noise:*** Comes from the environment
- ***Internal noise:*** Occurs in the sender's and receiver's mind

Noise in communication.

Are we communicating?



SOURCES OF NOISE

- 1) Absence of feedback.
- 2) Cultural differences.
- 3) Information overload.
- 4) Physical distractions.
- 5) Poor choice of channels
- 6) Semantic problems.
- 7) Status effects.

Noise in communication.

Are we communicating?



PSYCHOLOGICAL NOISE

- Mental interference that prevents you from listening
- Caused by conditions that affect our thinking and feeling
- ❖ If your mind is wandering when someone is speaking to you, the noise in your head is preventing communication.

TIPS TO IMPROVE OUR ACTIVE LISTENING



**Focus On The
Other Person**

1.



**Avoid
Judging**

2.



**Use Body
Language**

3.



**Avoid
Interrupting**

4.




**Respect
Silence**

5.

Stakeholder Engagement Strategy

- **Involve** stakeholders
- **Enable** appropriate management strategies
- **Create** and **maintain** relationships

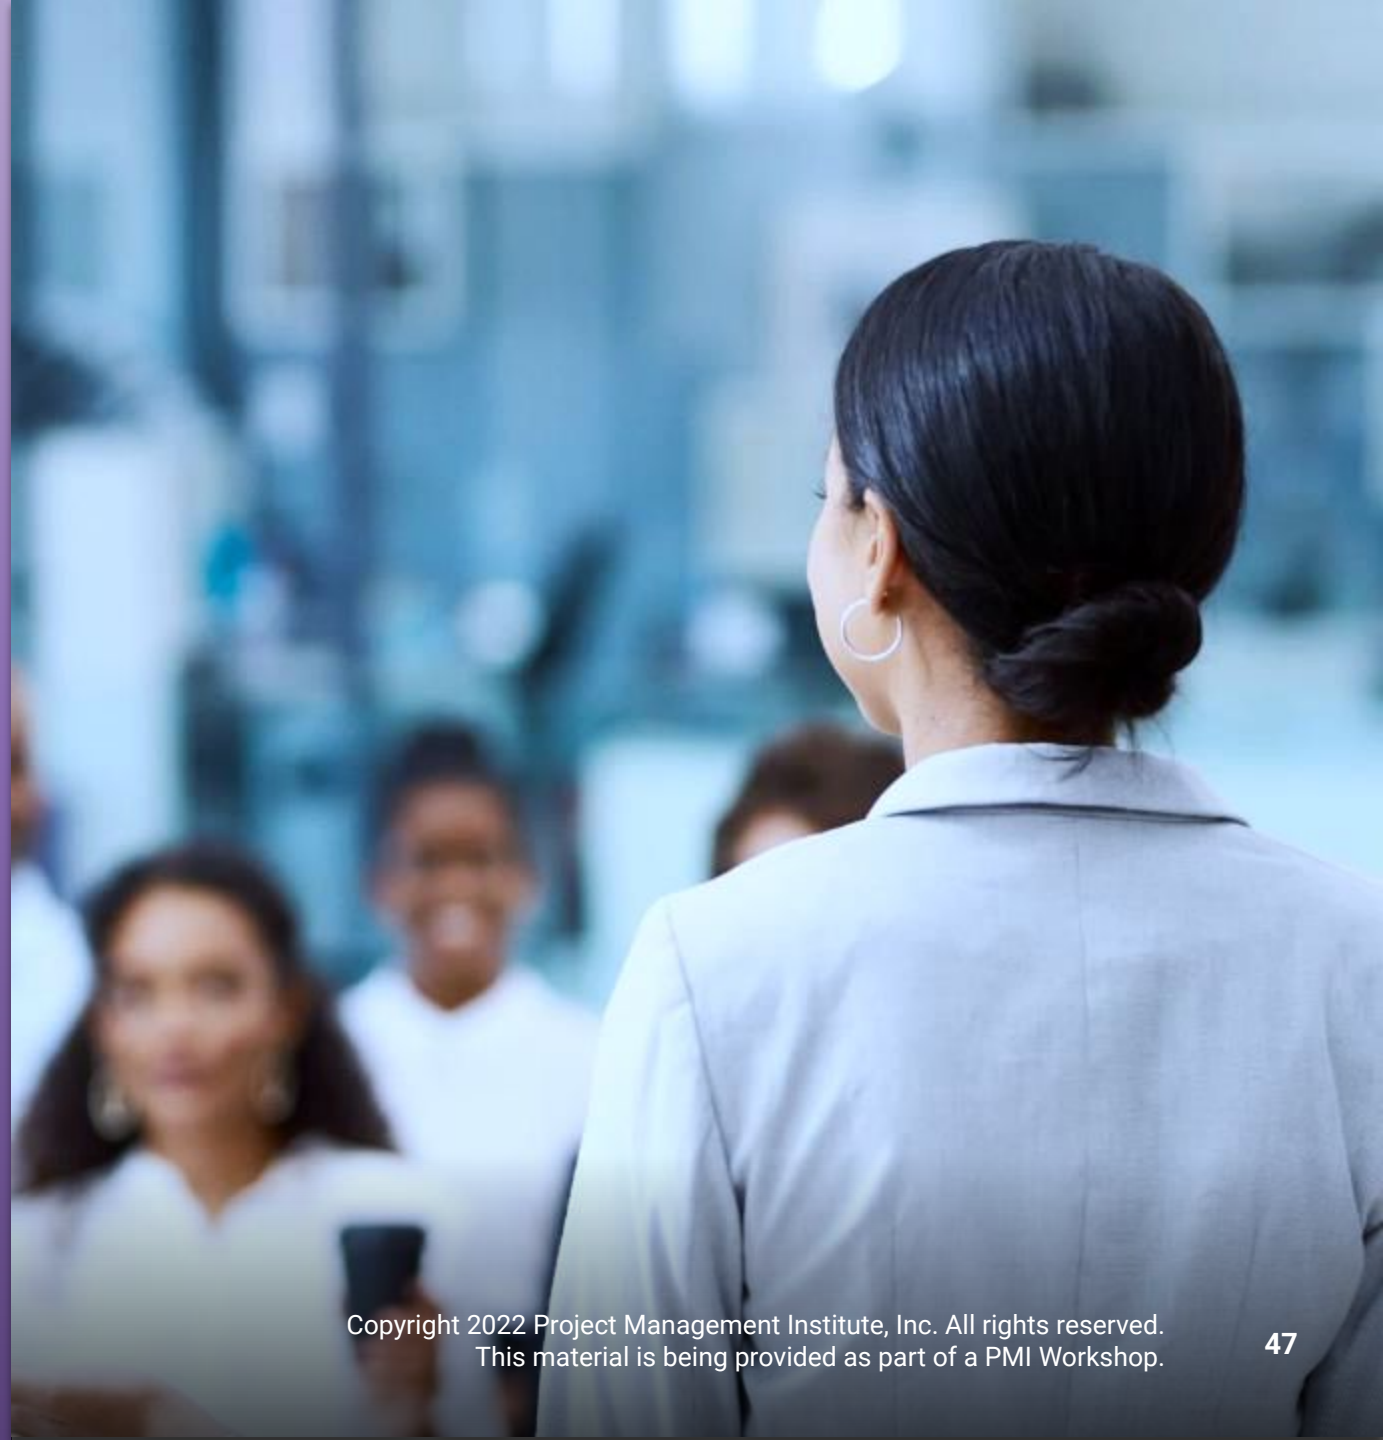

Feedback.

- Communication is a **two-way street**.
- Both **critical** and **affirming** feedback are key.
- Feedback **can be positive** if received and understood as intended.
- Feedback can be negative because of misunderstanding.
- No feedback provides an implicit acceptance of the message by the receiver.
- **Effective feedback** is clear, specific, and offered in a timely manner.



ECO Coverage

1.9 Collaborate with stakeholders







- Evaluate engagement needs for stakeholders (1.9.1)

2.4 Engage stakeholders

- Analyze stakeholders (power interest grid, influence, impact) (2.4.1)
- Categorize stakeholders (2.4.2)
- Develop, execute and validate a strategy for stakeholder engagement (2.4.4)

2.2 Manage communications

- Analyze communication needs of all stakeholders (2.2.1)
- Determine communication methods, channels, frequency and level of detail for all stakeholders (2.2.2)





Form the Team

TOPIC B

Lesson 2 Outline

- **Developing the Project team** – Build team agreements, structures and processes that support a culture that enables individuals to work together and benefit from interactions.
- **Project Team Formation** – *Key Concepts:*
 - Diversity and inclusiveness.
 - Cross functional team.
 - Using of virtual teams.
 - Co-locating teams.
 - Self-organizing teams.
 - Servant leadership.
 - Generalizing specialists/T-shaped skills. Tuckman's team development model and Team charter (team norms, ground rules).

Forming a Team.



Once you have a business case and have identified and assessed stakeholders, the next step is figuring out the team.

The goal is to create a high-performing, collaborative team environment that can execute the project objectives well.

Project teams are made up of individuals who wield diverse skills, knowledge and experience. **Project teams that work collaboratively can accomplish a shared objective more effectively and efficiently than individuals working on their own.**

In general: For a **predictive approach** – the team is assembled after the requirements are understood.

For an **adaptive approach**, the team is assembled initially and supports the project requirements.

Project Team Roles

- Project management staff
- Project work staff
- Supporting experts
- Business partners



Identify Project Resource Requirements Guidelines

If your project follows a predictive life cycle, these are a few of the major considerations you should think about when building a team.

- Will the team have **enough of the relevant skill sets** to perform the work and produce the desired results?
- Try to **avoid single points of failure** – i.e., only one resource has a needed skill to perform a particular type of work.
- Make use of what are called **generalizing specialists, who have a core competency but also general skills in other areas** that can be leveraged as needed by the team to support its objectives.
- In addition to the team members themselves, you will need to identify the **other physical supports that the team members will require** to be able to perform – equipment, access rights, etc.



Diversity, Equity and Inclusion Standards

- Teams are global and diverse in culture, gender, physical ability, language and many other factors.
- The project environment optimizes the team's diversity and builds a climate of mutual trust.



Experts and Expert Judgment.

Expert judgment is a technique that project managers can use to obtain additional guidance from individuals who are more experienced in various areas needed to be understood for the project.

People from other areas of the organization:

- *Consultants*
- *Stakeholders*
- *Professional and technical associations*
- *Historical data*
- *Project manager*



Project Team Formation

Key Concepts



CROSS-FUNCTIONAL TEAM

Teams that have all the capabilities to deliver the work they have been assigned.

Self-organizing team: A **cross-functional team** in which people fluidly assume leadership as needed to achieve the team's objectives.

Servant leadership: The practice of leading the team by focusing on understanding and addressing the needs and development of team members in order to enable the highest possible team performance.




These concepts can be applied in any kind of project team.

Create a Collaborative Team Culture




(Optional)

How do you think a collaborative team culture can be created in a hybrid approach? Give some examples!



Project manager:

- Builds team agreements, structures and processes that support a culture that enables individuals to work together and benefit from interactions
 - Tailors a **resource management plan**
-



- The team assembles and self-organizes to support project requirements.

Project Team Formation Video

Tuckman's Ladder of Team Development

Dr. Bruce Tuckman



Bruce Tuckman's Stages of Team Development.



Forming

Team members meet and begin to trust one another.

Storming

Team members begin to assert themselves and take control of emerging issues.

Norming

Team begins to work productively, without worrying about personal acceptance or control issues.

Performing

Team is working at optimum productivity and is collaborating easily, communicating freely, and solving its own conflicts.

Adjourning

Team members complete their assigned work and shift to the next project or assigned task.

Tuckman's team development model.

Stage	Characteristics	Project manager/team leader role.
Forming	Team meets (formation); begins collective work.	Outlines mission; looks for agreement on team roles, rules, guidelines for decision making.
Storming	Team deals with confusion and conflict over goals and decision making, roles and control.	Facilitates discussion; ensures common understanding of agreements.
Norming	Team accepts goals, roles, rules; works positively.	Encourages norming process; supports and coaches; celebrates success.
Performing	Team focuses on achieving goals; personal growth for team members; conflict handled positively.	Encourages high performance; facilitates communication; celebrates success.
Adjourning	Shifting from project tasks to closure process.	Recognizes individual and team efforts.

RACI Chart



DEFINITION

A common type of responsibility assignment matrix (RAM)
Responsible, Accountable, Consulted, and Informed statuses define the involvement of stakeholders in project activities.

Responsibility Assignment Matrix - RACI Chart.

- **The RACI model is a quick way to lay out roles and responsibilities on a project.** It allows the team to discuss, communicate and agree upon the project roles. **RACI** is an abbreviation that stands for:
- **Responsible (R)** – the person who actually owns the project, task, or work. This could be a task team leader.
- **Accountable (A)** – the person who will sign off on the work and judges its completion and how it meets quality standards. This could be the Project Sponsor or whomever has final sign-off authority.
- **Consulted (C)** – the person who has the ability or special knowledge needed to complete the work. These can be Stakeholders, Subject matter experts, or anyone else who is key to completing the work.
- **Informed (I)** – people who must be kept informed of the work, but not necessarily consulted.

RACI Chart

Activity	Project Sponsor	Project Manager	Project Team	Department Manager
Prepare Bill of Materials		A	R	C
Prepare Estimate	I	A	R	I
Authorize Expenditure	R	I	I	I
Send Procurement Documents		R	C	
Evaluate Bids	A	R	C	
Perform Inspections	I	A	R	

R = Responsible A = Accountable C = Consult I = Inform

Project tasks	Senior Analyst	Project Manager	Head of Design	SVP Finance	SEO Lead	Sales Director	Senior Management
Phase 1: Research							
Econometric model	R	I	I	A	C	I	I
Strategic framework	A	I	I	R	I	I	C
Risk factors	R	I	I	A	I	I	I
Phase 2: Structure							
Product specs	I	A	R	I	C	C	C
Design wireframe	I	C	R	I	C	I	C
User journey	I	C	R	I	C	C	C
User experience testing	I	C	R	I	C	C	C
Evaluation framework	I	R	C	I	C	I	C
Development backlog	I	R	C	I	C	I	C
Delivery roadmap	C	R	A	C	C	C	I

WBS Element	Project Team Members					Other Stakeholders		
	I.B.You	M. Jones	R. Smith	H. Baker	F. Drake	Sponsor	Clnt Mgt	Func Mgt
I.0.1.1 Activity A	N				R			
I.0.1.2 Activity B		R	C					
I.0.1.3 Activity C	R		S			A		G
I.0.2 Activity D			R		S			A
I.0.3.1 Activity E			R			N		
I.0.3.2 Activity F				R				
I.0.3.3 Activity G	R			S		A	A	
I.0.4 Activity H		R			C	N		

Key: R = Responsible, S = Support Required, C = Must Be Consulted, N = Must Be Notified, A = Approval Required, G = Gate Reviewer

Project Manager Role in Adaptive Teams




Leadership and management models:

- **Centralized:** All team members practice leadership activities and accountability is usually assigned to one individual, such as the project manager or similar role (**Team lead**).
- **Distributed:** One project team member (may shift) serves as facilitator to enable communication, collaboration and engagement on accountable tasks.
- **Some agile practitioners think the role of a project manager is not needed, due to self-organizing teams taking on the former responsibilities of the project manager.**
- However, pragmatic agile practitioners and organizations realize that project managers can add significant value in many situations. The key difference is that their roles and responsibilities look somewhat different.

Hybrid Team Formation

Example:

Centralized coordination by a project manager or team lead and self-organized project teams for portions of the work.

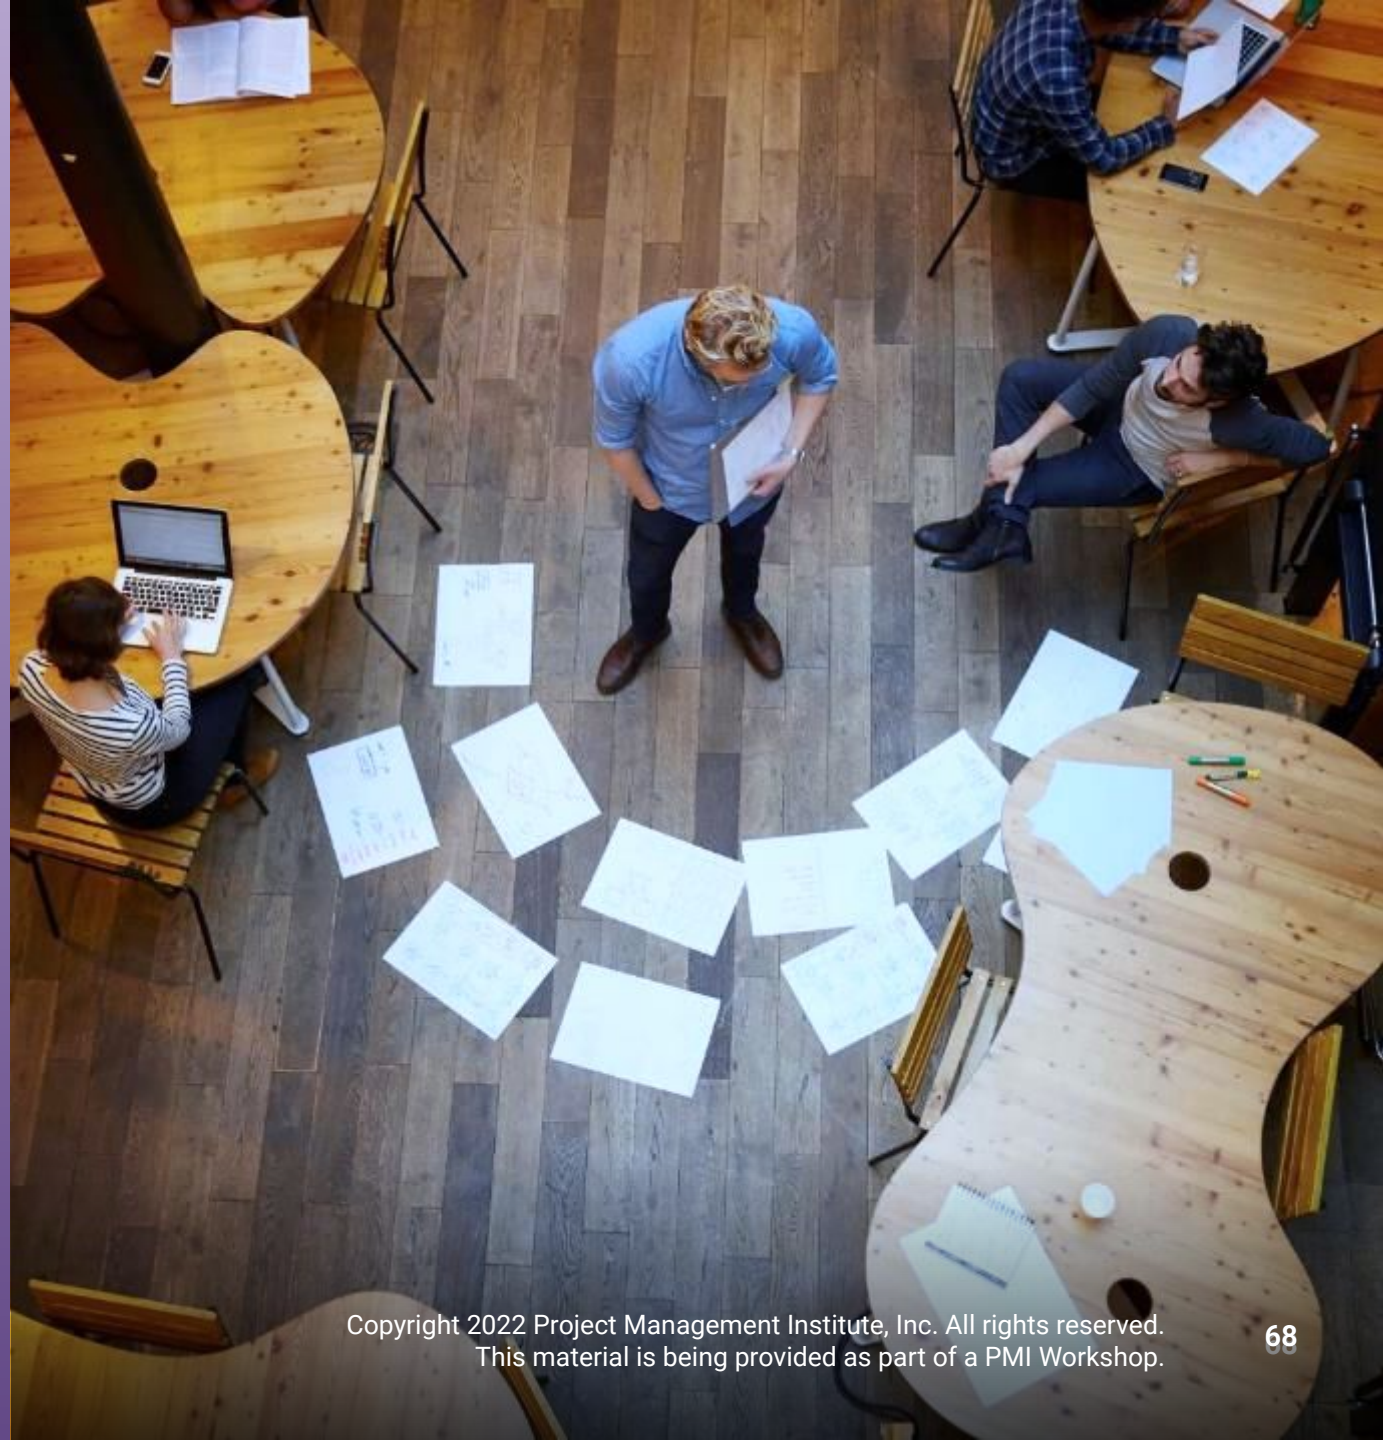

Project Team Composition

-
- Refers to team's makeup and how team members are brought together
 - Varies based on organizational culture, location and scope
 - Can be full-time or part-time members
 - Includes varied knowledge and expertise — i.e., generalists and specialists


Negotiation Skills

Includes internal and external conversations towards reaching agreements.


Determine reliable methods to ensure communication is aimed at reaching consensus. This keeps the team culture healthy.

Team members might negotiate:

- ✓ Roles and responsibilities
- ✓ Priorities
- ✓ Assignments

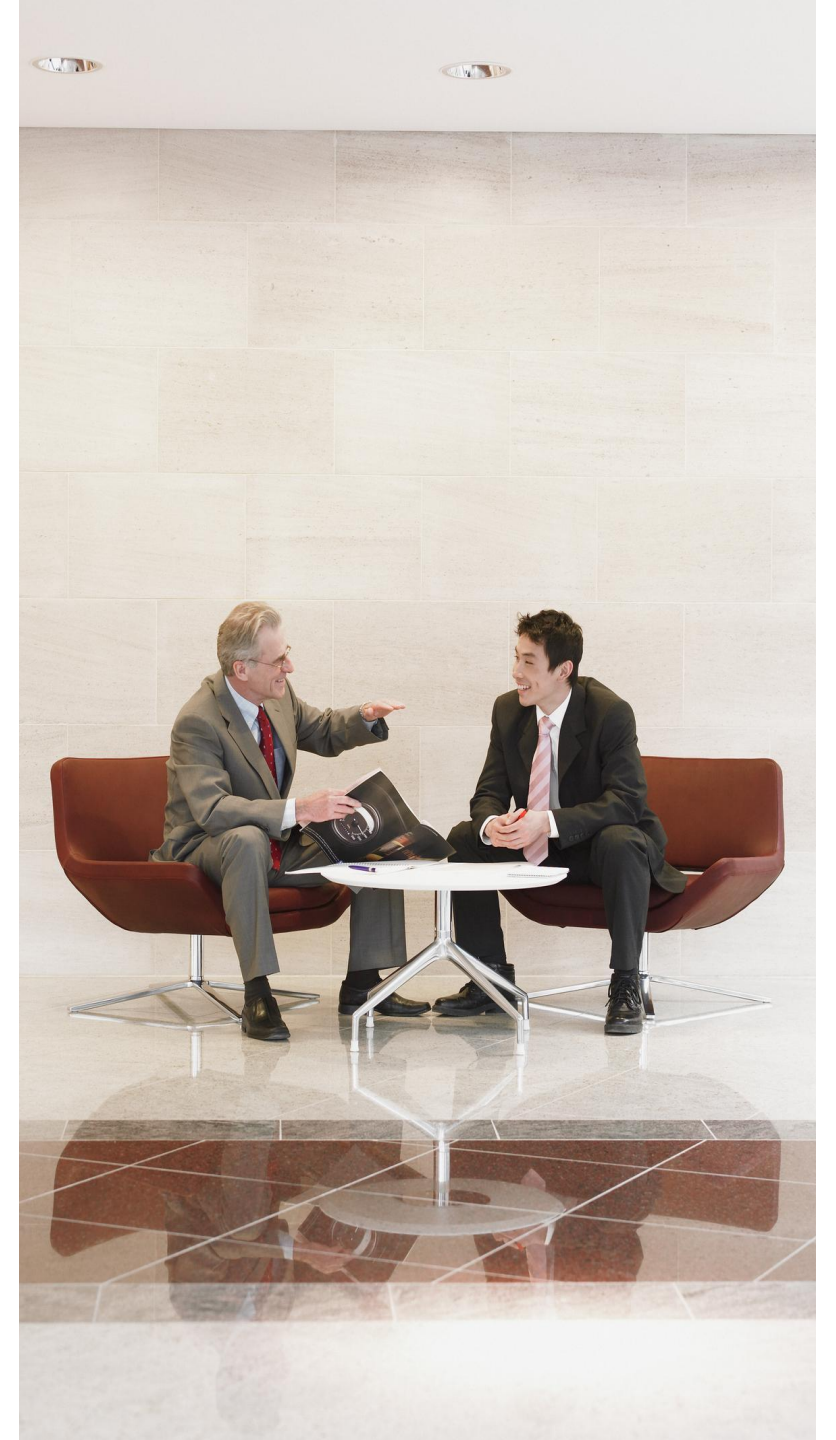


Project Organizational Chart

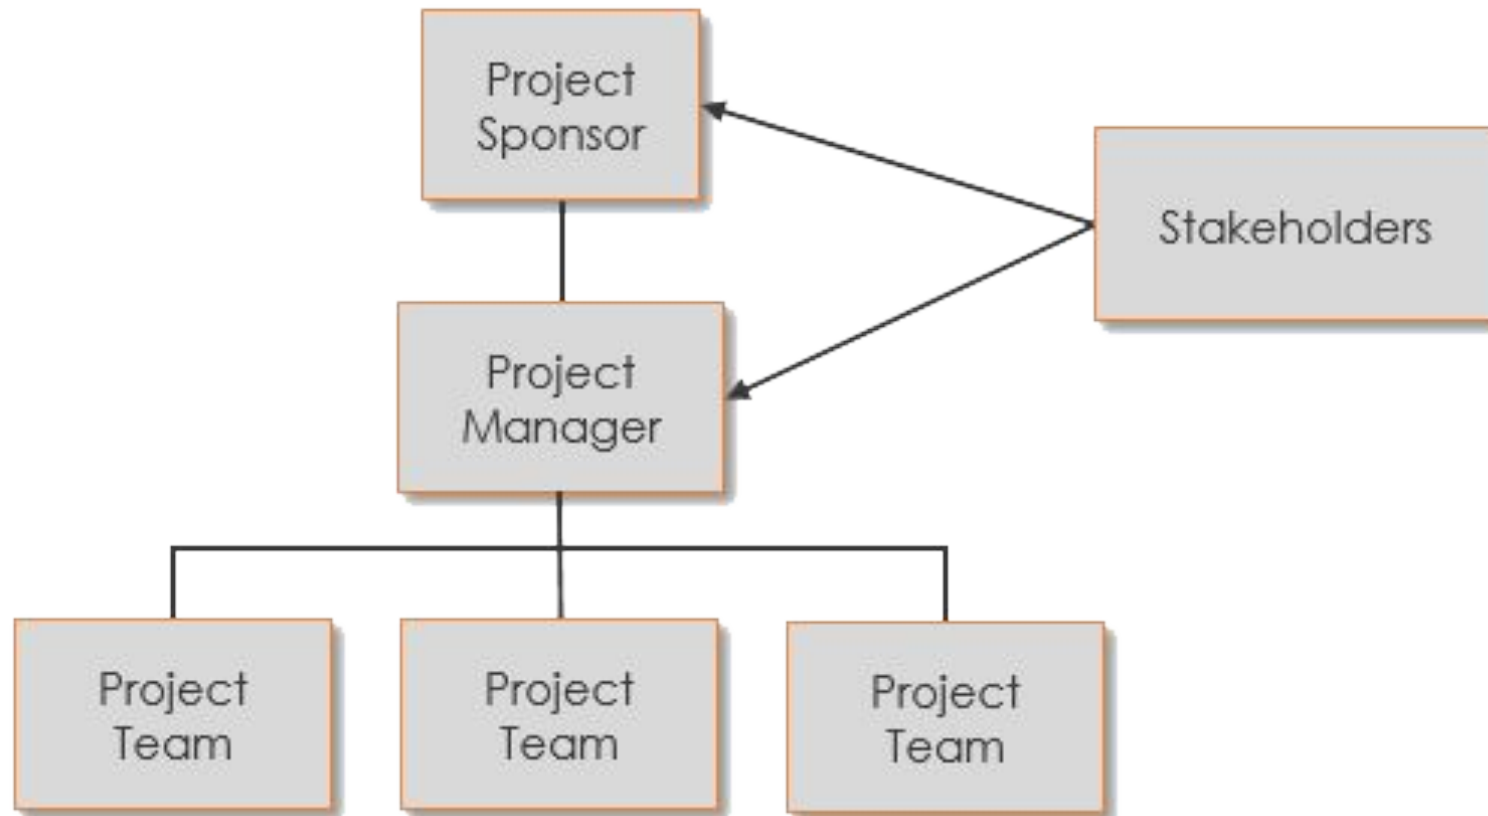

Identify Project Resource Requirements Guidelines


GENERALIZING SPECIALISTS: Refers to a project team member who has a particular area of deep expertise but also has experience in many other areas that may not be directly related to their core area. These team member types are valued on agile projects because of their ability to be interchangeable.

T-SHAPED: Refers to a person whose skill set comprises one area of specialization and broad ability in other skills required by the team.

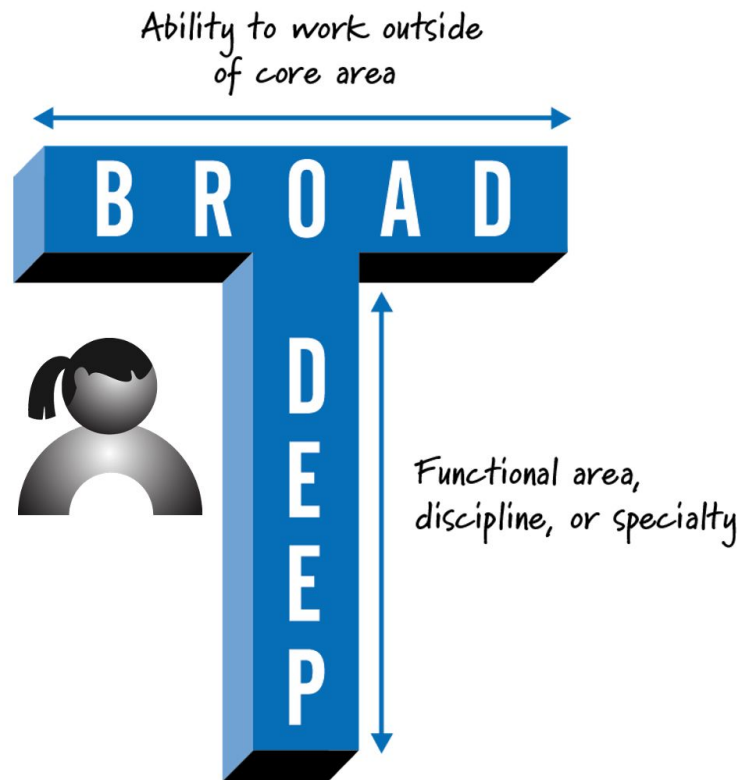


T-Shaped People and Self-Organizing Teams

- Provide individual value and versatility on project teams
- Lend flexibility to organizations
- Help avoid key resource shortages or work stoppages due to availability
- Train and coach team members to become T-shaped, combining **breadth** and **depth** of knowledge



Focus on Team Strengths

- A SWOT analysis is appropriate for use in identifying the strength and weakness. This will enable you to **focus on team strengths!**
- In addition, you should identify any **challenges** that the team will need to overcome to obtain better performance and any **opportunities** that can position the project advantageously.
 - Organize around team **strengths**
 - Be aware of **weaknesses**
 - Identify **threats** to team success and **opportunities** to improve team performance.

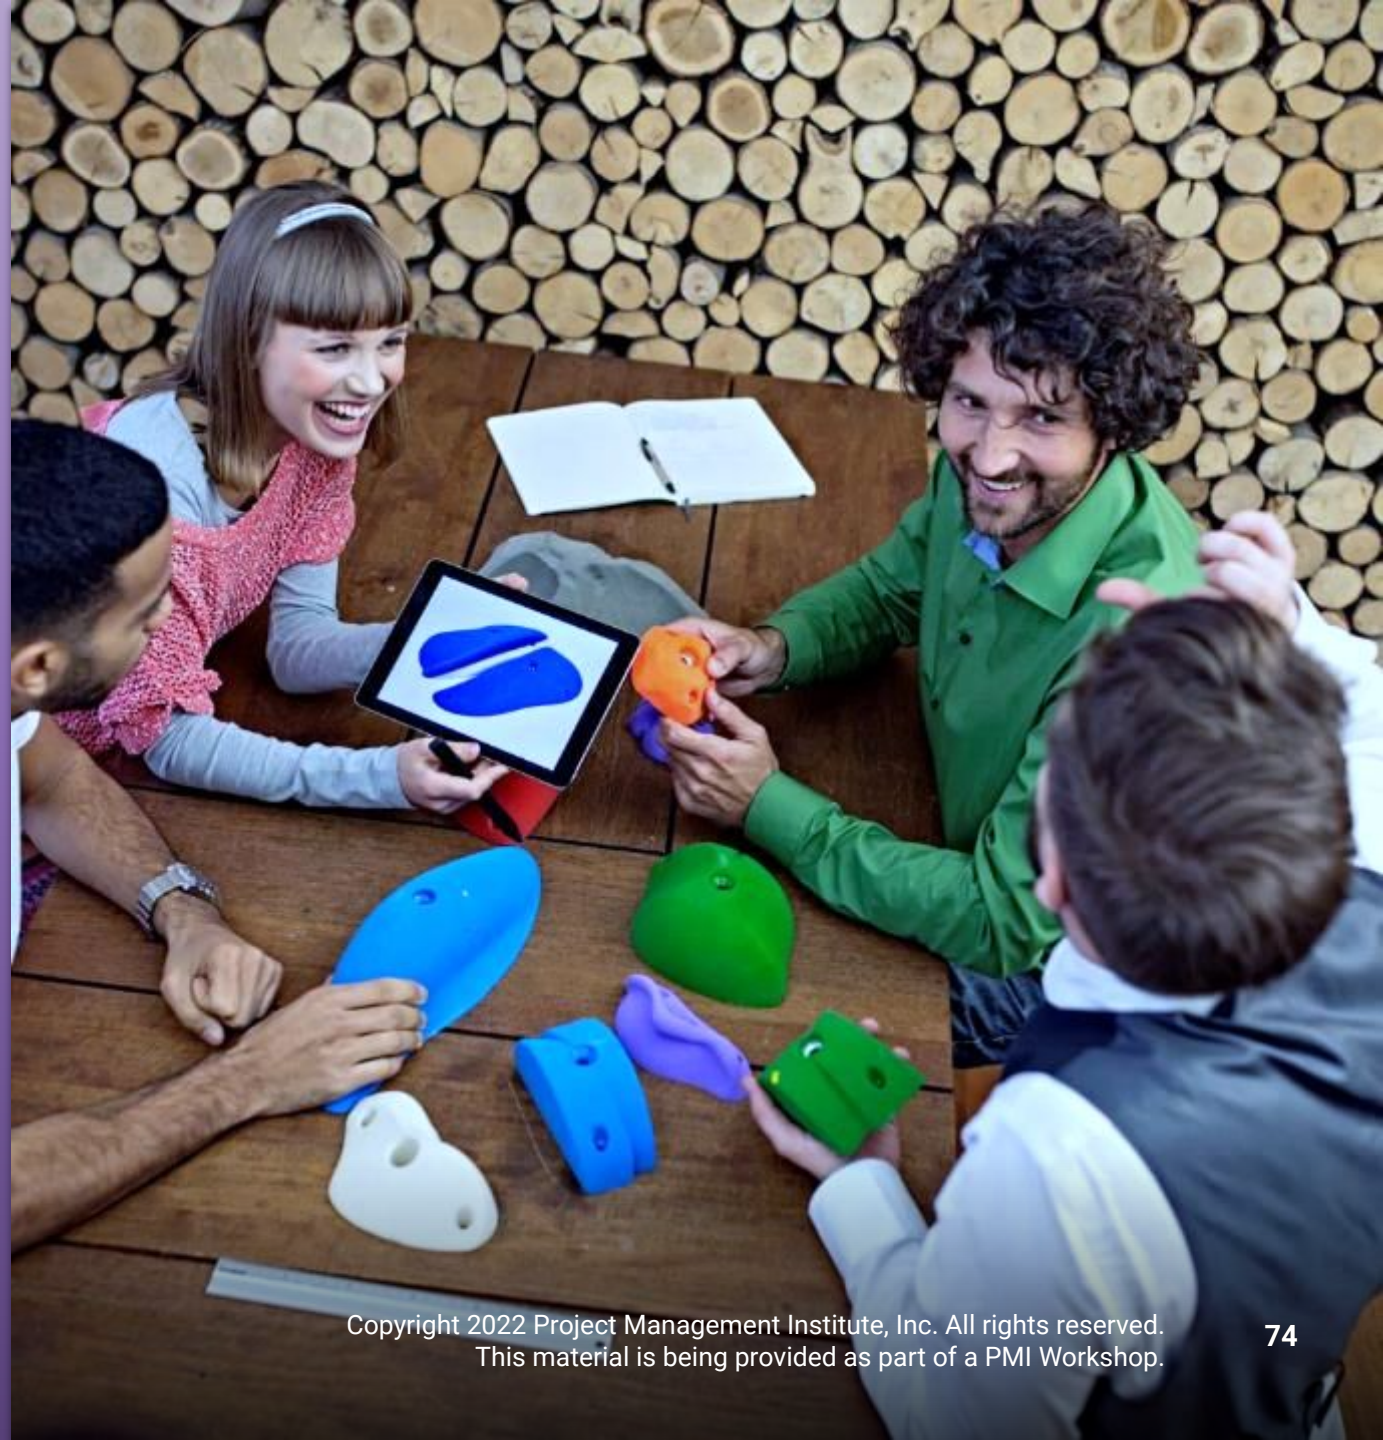

Team Norms.

Team norms are a shared set of mutually agreed rules. It's a means of keeping a standard and accountability in case of problems.

Team norms are the agreed standards of conduct for all team members. Establish these norms together early in the project to set the stage for an appropriate range of behaviors and actions.

- Together, **establish** expected team behaviors **at the beginning of the project**. Enable teams to **handle challenges** later.
- Include guidelines and techniques for:
 - Meetings
 - Communications
 - Conflict management
 - Shared values
 - Decision-making
- Align team values with the *PMI Code of Ethics and Professional Conduct*

Team Charter



DEFINITION

A document that enables the team to establish its values, agreements, and practices as it performs its work together.


Ground Rules

Includes what's acceptable and unacceptable for team behavior

Benefits:

- ✓ Sets performance and communication expectations
- ✓ Decreases risk of confusion
- ✓ Improves team performance

Team Charter* and Ground Rules*



- A document – electronic or paper, or a poster of the ground rules.
- Created together with the team
- Includes:
 - *Shared values*
 - *Behavior guidelines*
 - *Guidelines for communications and use of tools*
 - *Decision-making guidelines*
 - *Performance expectations*
 - *Conflict-resolution measures*
 - *Meeting time, frequency, and channel*
 - *Other team agreements – e.g., shared hours, improvement activities*

Team Communication

Effective communication includes:

- *Verbal*
- *Written*
- *Behavioral*
- *Physical (notice boards)*
- *Virtual*

- Teams are successful by working together to execute work, solve problems and produce solutions. **In a virtual team**, the need for effective communication is even greater due to the lack of opportunity for osmotic learning from just being around your other team members.
- Part of an effective **team charter** is to make decisions as a team about how, when and why you communicate with one another, and what the shared expectations are. Include communication expectations and details in the **team charter**
- Organize communications:
 - Facilitate team and stakeholder collaboration Manage expectations
 - Check regularly to make sure it's working!
 - Plan and use **retrospectives** to discuss communications improvements

Co-located, Virtual or Both?



*What kind of team
are you on?*



Virtual Team: *A group of people with a shared goal who fulfill their roles with little or no time spent meeting face-to-face.*

- “Normal” in most workplaces
- Create opportunities for the organization:
 - Better skills at lower costs
 - Avoids relocation expenses
 - Work/life balance
- Rely on communication technology
- May have bonding challenges

Colocated Team: *An organizational placement strategy in which the project team members are physically located close to one another to improve communication, working relationships, and productivity.*

- Interaction is easy
- Better bonding is facilitated
- Use of physical tools, collaboration and boards possible


Virtual Team Challenges

Individual performance tracking

Diversity - language, technological skill

Solo working prohibits bonding

- It can be challenging to form and manage, for several reasons, including:
 - ***Bonding and team identity can be hard*** to create when team members are geographically dispersed.
 - ***Communication and information*** sharing must rely on various forms of technology because teams cannot meet face to face.
 - ***Because roles, reporting and performance can be harder to track*** on a dispersed team, individual contributions may be overlooked.

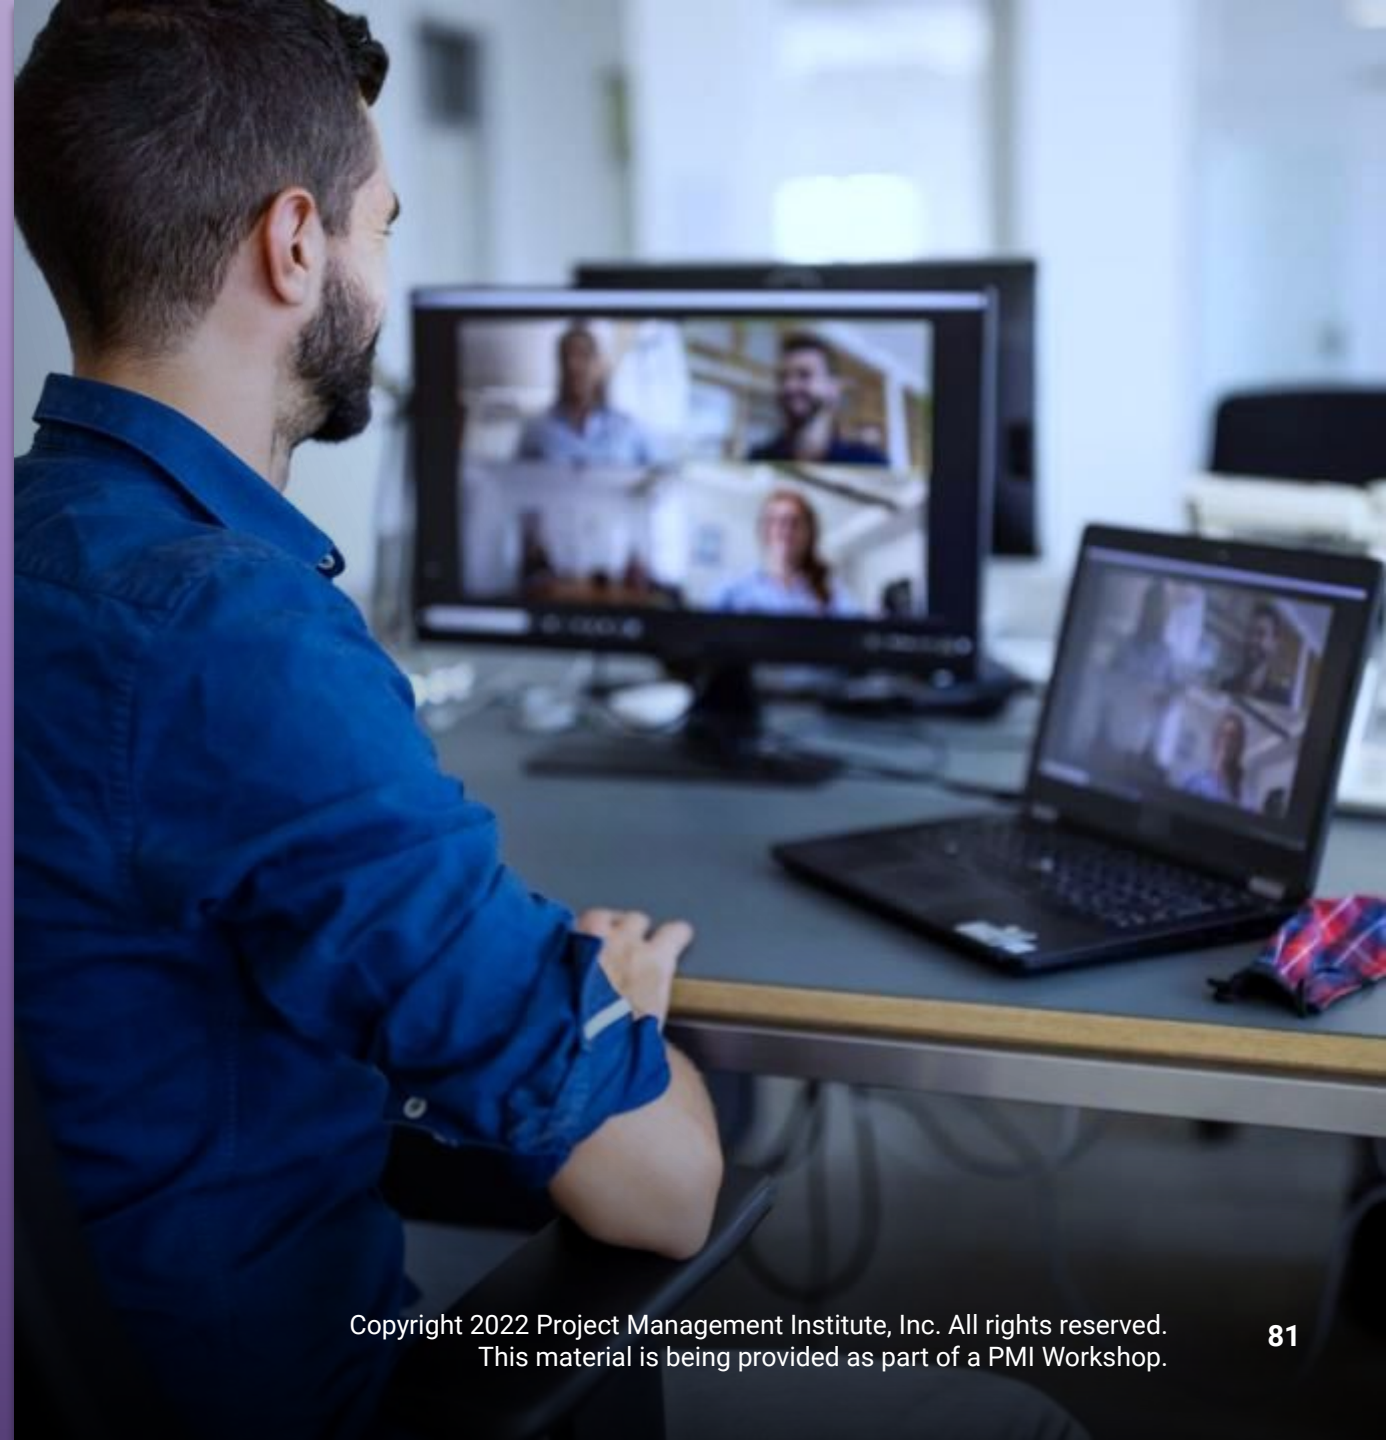


Running Virtual Teams

- Check in with people individually as often as possible
- Conduct positive network-building activities




What are your tips for creating a positive virtual team experience?

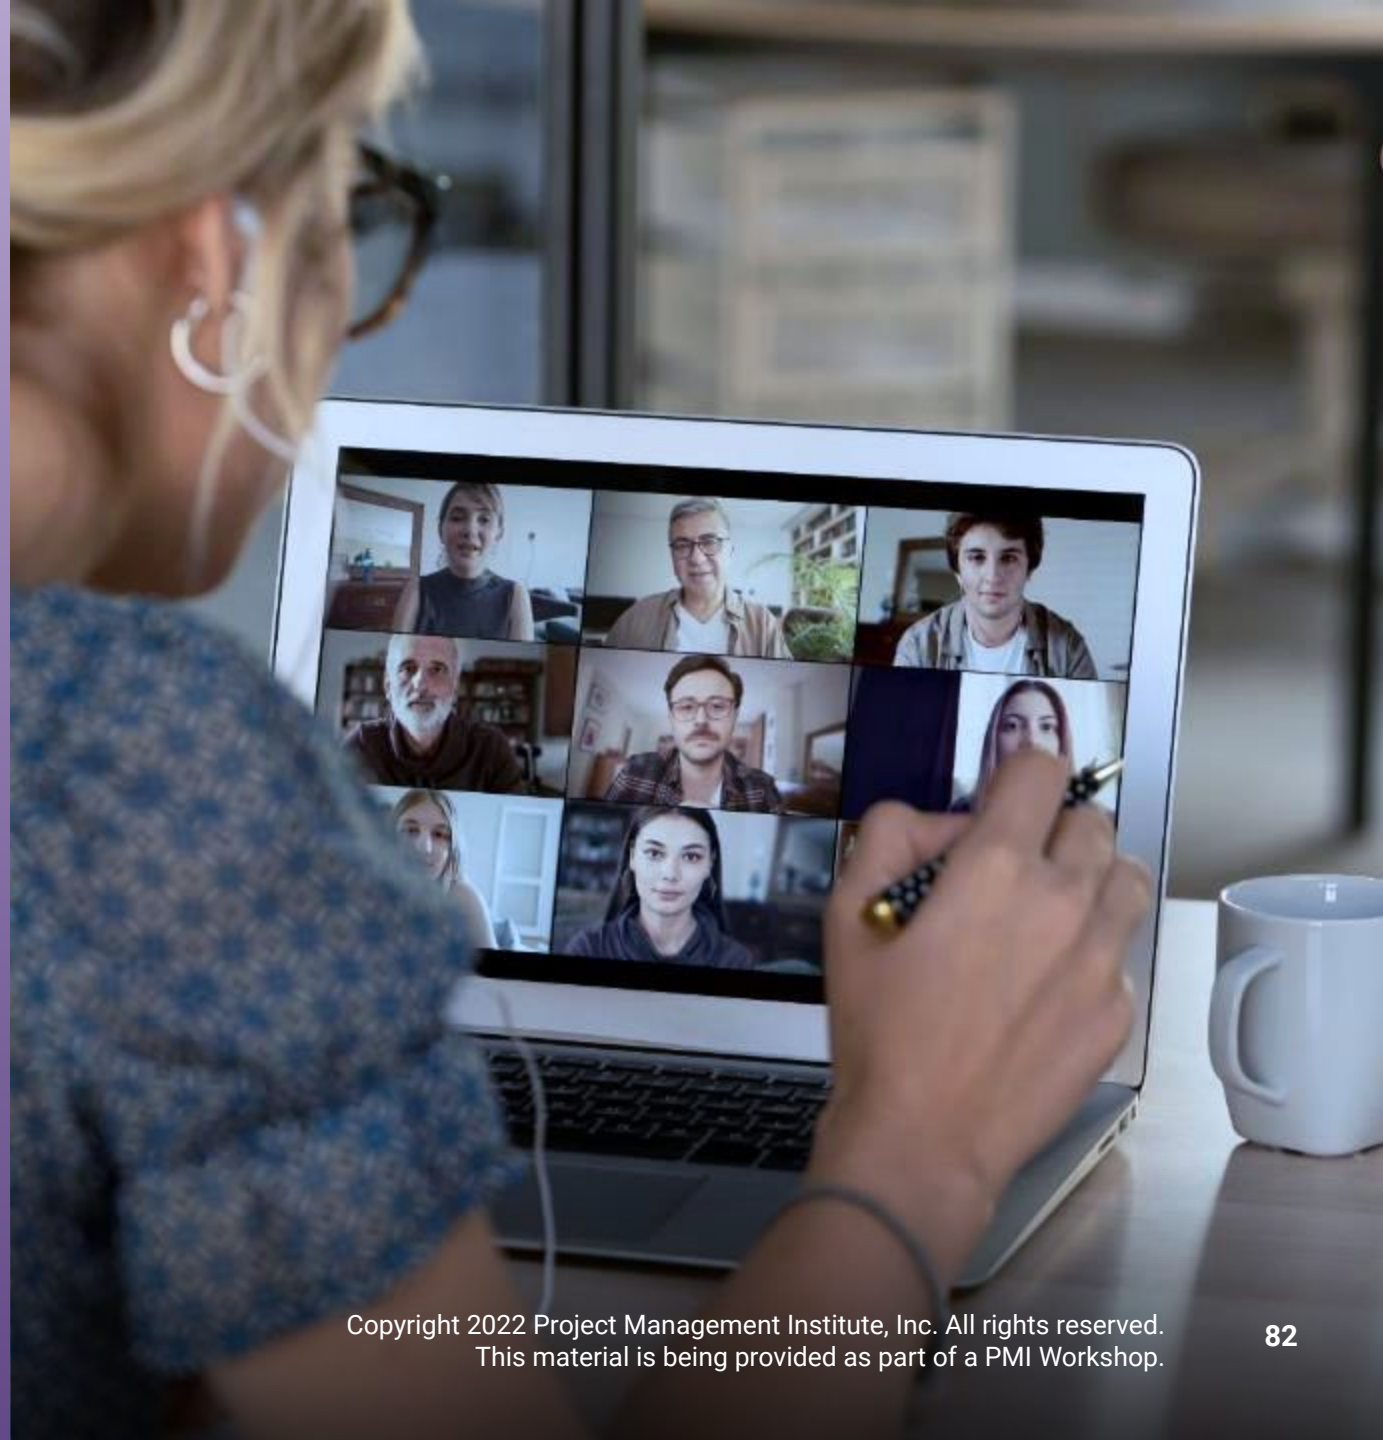

Virtual Team Communication Technology.

- Plan team communication and collaboration methods
- Consider working hours, geographical dispersion and security requirements
- Use appropriate tools:
 - Task boards
 - Messaging and chat
 - Calendars
 - Document storage
 - Knowledge repositories
 - Videoconferencing

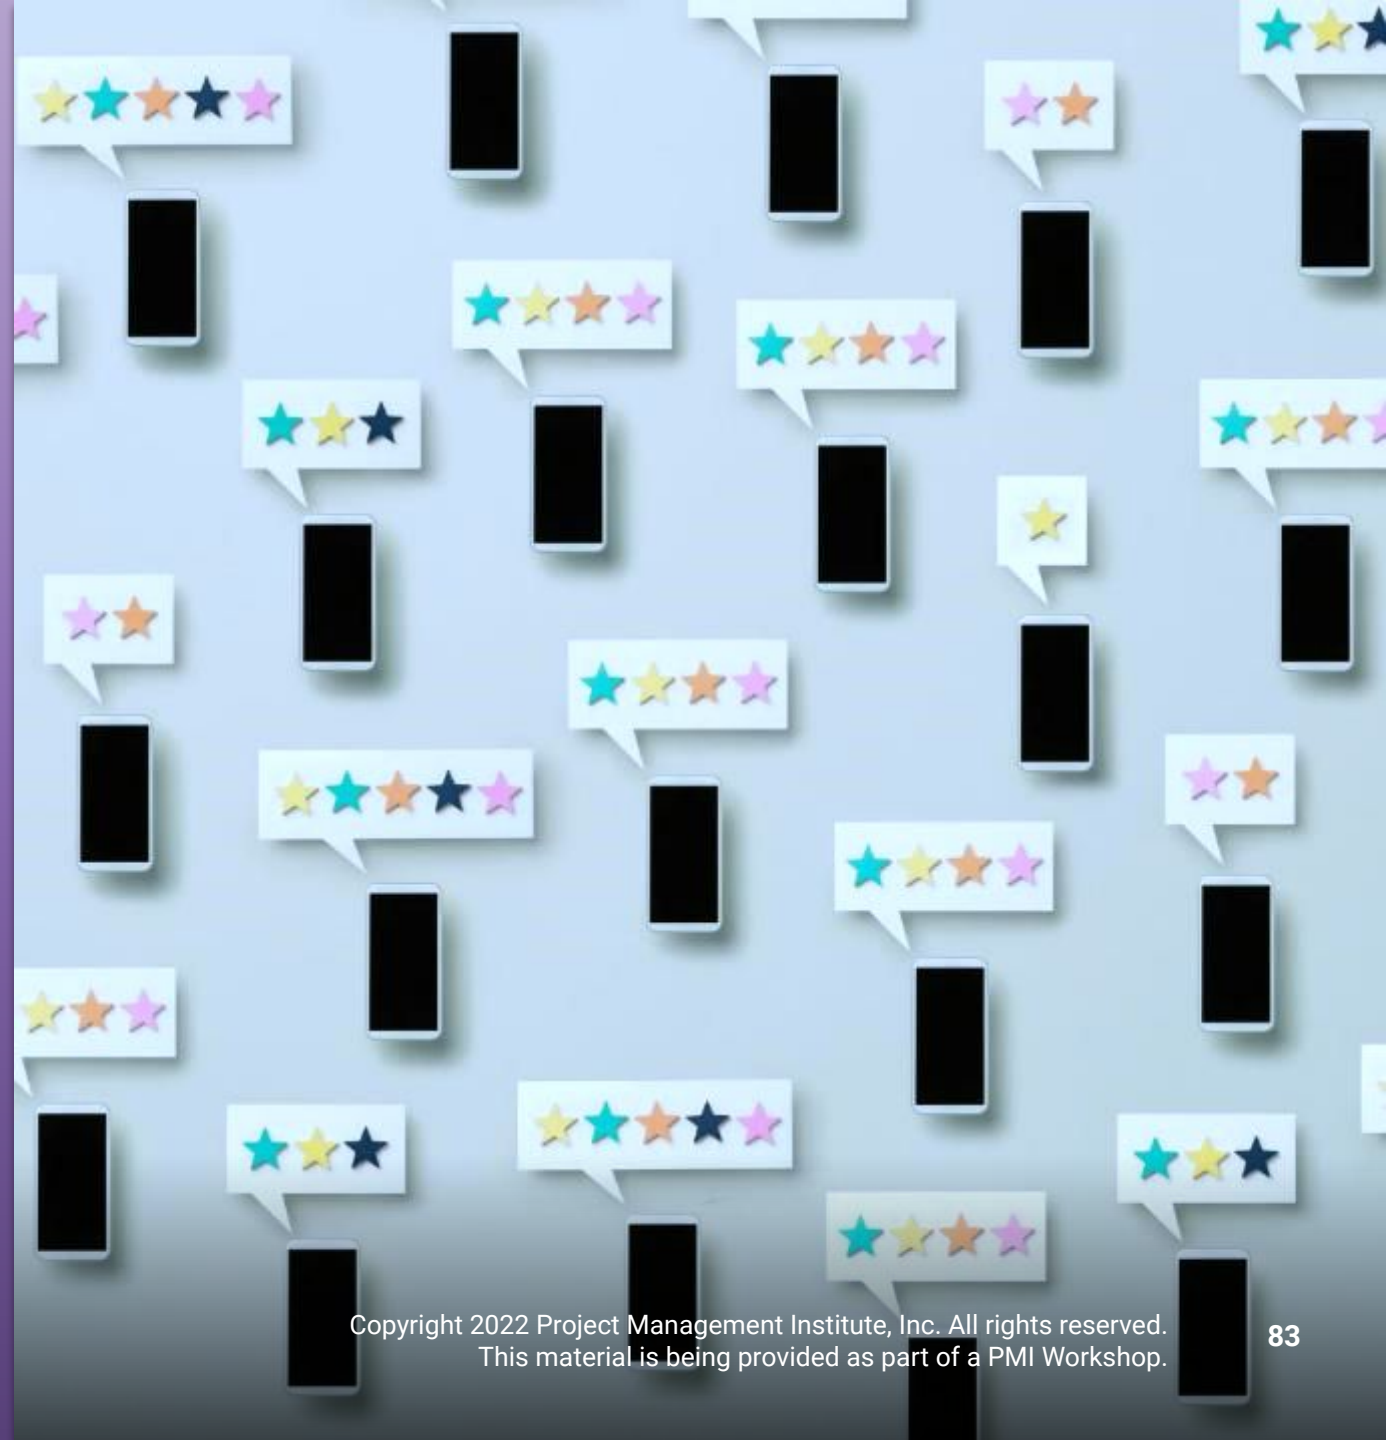

Address Virtual Team Member Needs

Facilitate and ensure collaboration as a priority

Address the basic needs of a virtual team, including:

- Cohesion
- Shared goals
- Clear purpose
- Clarity on roles and expectations



Nurturing Team Performance

Ensure the team has the **knowledge, skills, attributes, and experience** required to produce positive project outcomes.



Gain a better understanding of customer needs and team capabilities to **identify gaps in the team's skill set**.

Check for these gaps frequently and seek to close them. Try:

- ✓ New or better resources
- ✓ Training to enable the team to develop missing skills
- ✓ Additional customer engagement to gather data



ECO Coverage



1.4 Empower team members and stakeholders





- Organize around team strengths (1.4.1)

2.16 Ensure knowledge transfer for project continuity

- Discuss project responsibilities within team (2.16.1)
- Outline expectations for working environment (2.16.2)

1.11 Engage and support virtual teams

- Examine virtual team member needs (e.g., environment, geography, culture, global, etc.) (1.11.1)
- Investigate alternatives (e.g., communication tools, colocation) for virtual team member engagement (1.11.2)





Build Shared Understanding

TOPIC C

Lesson 2 Outline

- **Build a Shared Understanding** – Seek Consensus among the Team and Stakeholders. Share the project agreements (vision statement and project charter) with stakeholders and the team.
- Use interpersonal and leadership “power skills” and open communication channels with stakeholders and team members.
- Use a project charter and Kick-off meeting.

Building a Shared Understanding.

- One of the first goals in starting a project is to ensure that all team members and stakeholders have a common understanding of the objectives of the project, as well as an understanding of any agreements, such as contracts or statements of work that initiated the project.
- You must also enable the team to understand the importance of the project and the alignment to the organization's strategic objectives.
- Again, the focus is on creating that collaborative team environment, but the stakes are highest in this period. **As much as possible, you need to make sure everyone is aligned before work starts.**
- If you get the team in a good place from the start, then keeping them motivated and inspired to do their best work will be easier in the weeks ahead!

Seek Consensus for the Project Among the Team and Stakeholders.

- Demonstrate leadership behaviors
- Focus on value.
- Be a diligent, respectful and caring steward.
- Navigate complexity.
- Embrace adaptability and resiliency.

Create artifacts:

- Project charter.
- Project vision statement.




Building a Shared Understanding

Guidelines

- **Share** the project agreements (vision statement and project charter) with stakeholders and the team
- **Agree or negotiate** to reach agreement and “buy-in”:
 - Project agreements — stakeholders
 - Roles and responsibilities, priorities and assignments — team
- **Uphold** the agreements throughout the project



Use open and reliable communication methods and your leadership “power skills”

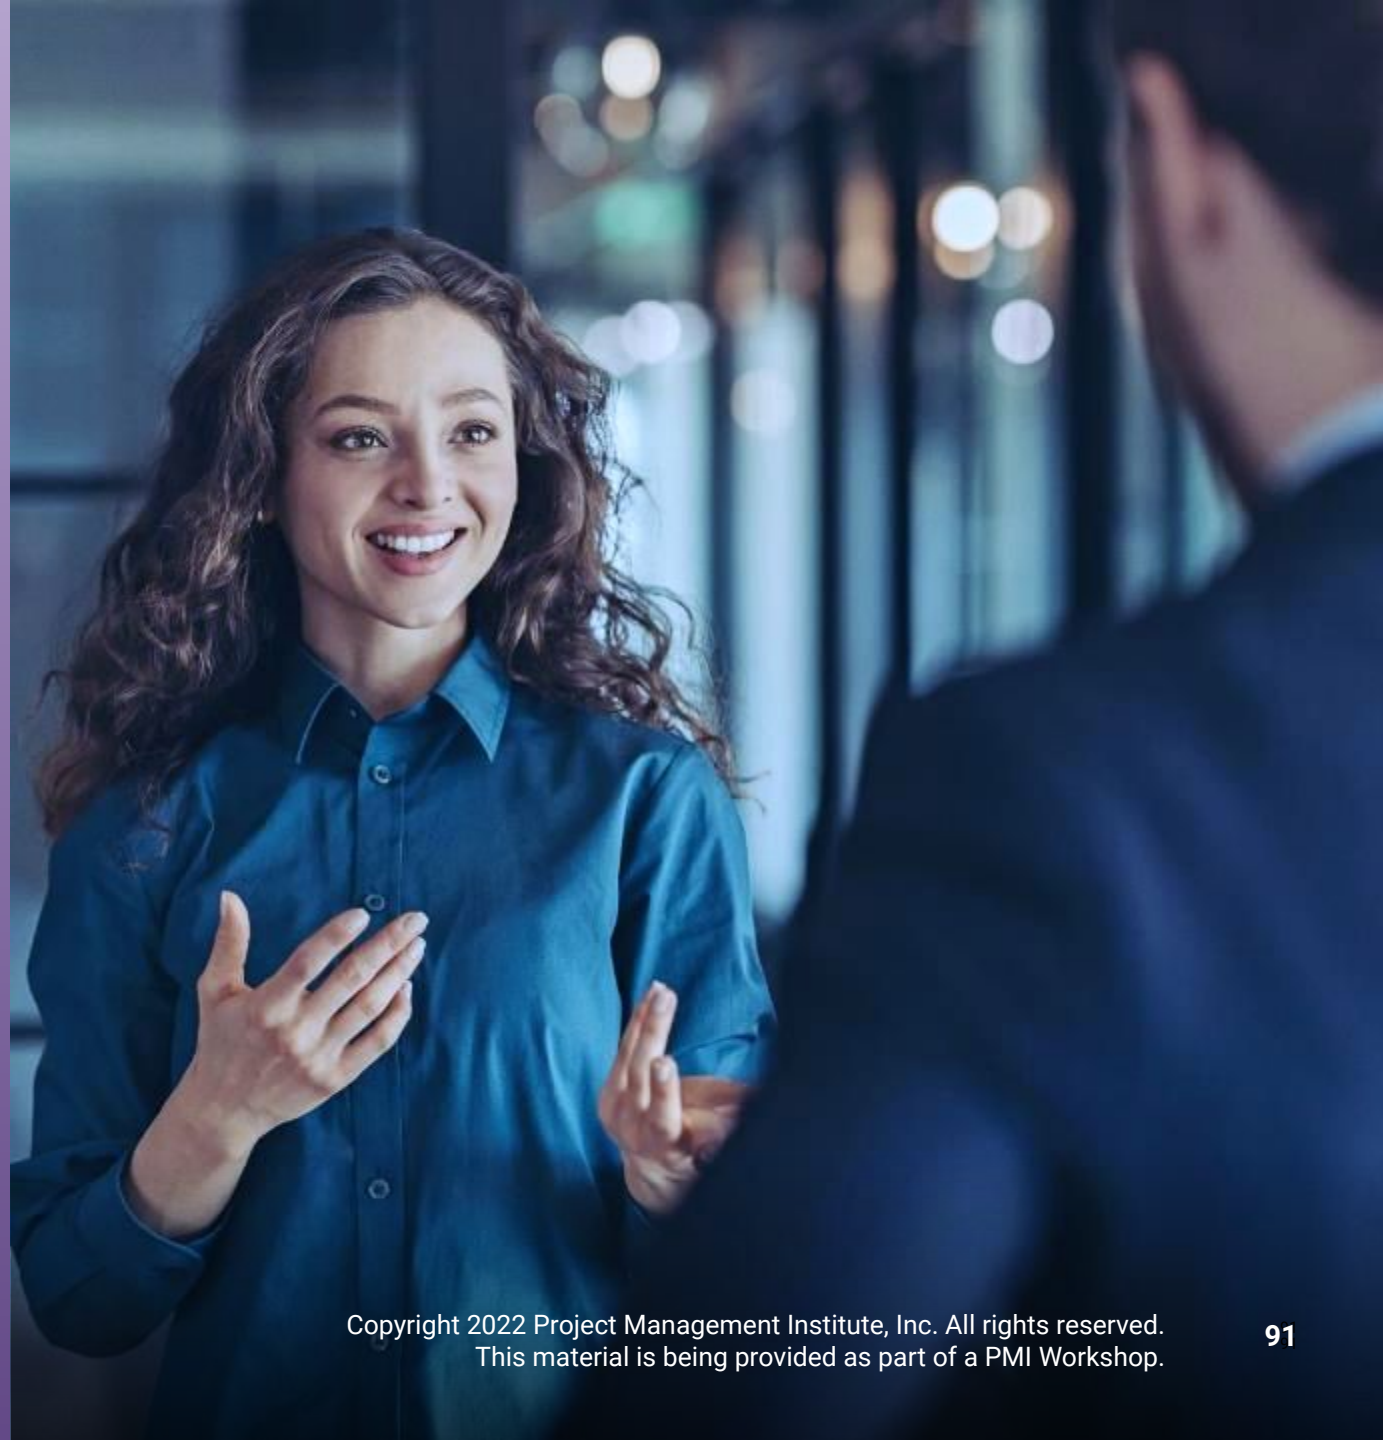

Project Vision Statement

- When a project begins, it is critical to have a clear vision of the desired objectives and alignment with the organization's strategic goals.
- This includes the creation of a **vision statement**.
- **It is created by the product owner, sponsor or key stakeholders** and continually be reinforced to the team throughout the project.
- There are many ways that this vision statement can be expressed and understood.
- Refer to it throughout the project to maintain alignment.

Holistic Understanding of the Project Negotiation Goals

First, find out...

- The **boundaries of negotiation** for the project agreement
 - What, if anything, is eligible for discussion or troubleshooting
- The **ultimate objectives** of the project

Then:

- Apply critical thinking and business acumen
- Discover how the project fits in the organizational landscape and business objectives

Exercise: Understanding Business Objectives

Project vision: This is a flagship project for Shawpe as it begins regional growth/expansion. More community–commercial (C4C) partnerships will be formed in the near future.

Mission: Commercial real estate development

Objectives:

- Revitalization of historic downtown area, establish community–commercial space
- Profitable community partnership with Oasestown Municipality

Goals:

- Construction of centre, including sensitive restoration of historic structures
- Successful marketing of centre to tenants, profitable rental income
- Establish property management franchise model with Oasestown Municipality

Strategies:

- Diversify project portfolio to include historical conservation work
- Establish community development as part of Shawpe brand

How to Create a Holistic Understanding of the Project

- **Ask stakeholders** to elaborate and clarify their vision or inputs, including asking the sponsor to clarify the vision statement!
- Existing **agreements** may contain initial intentions for, or describe, a project:
 - Contracts with external parties
 - Memorandums of understanding (MOUs)
 - Service-level agreements (SLAs)
 - Letters of agreement or intent
 - Verbal agreements
 - Communication (especially emails) between key stakeholders
 - Statements of work (SOW)

Refer to Business Case & Business Needs Documents.

Business case:

- A documented economic feasibility study
- Establishes benefits of project work
- Provides a basis for authorization of further project activities

Business needs documents:

- Identifies high-level deliverables
- A prerequisite of a formal business case
- Describes requirements — what needs creating and/or performing

Negotiate and Agree on Project Success Criteria.

KEY PERFORMANCE INDICATORS (KPIs)

A set metric used to evaluate a project, an organizational unit, or a project team's performance against the project vision and objectives. KPI can be time bound.

- Interview **stakeholders**
- Gather **expert judgment** on technical success criteria
- Check:
 - Organizational (program, operations) **key performance indicators (KPIs)**
 - Lessons learned and historical data
 - Quality policy
 - User acceptance testing (UAT) requirements



- *Reporting and verification criteria for objectives*
- *Identification of deliverable and objective **acceptance criteria** for each*



- *A **definition of done (DoD)** may be specified for the project, in addition to iteration outputs*

Help Everyone Understand the Vision Guidelines



- Use interpersonal and leadership “power skills” and open communication channels with stakeholders and team members
- Get creative with agile methods!
 - A **product box exercise** to internalize the vision from the customer’s point of view and emphasize product/project value
 - **Example:** Here is why Oasestown residents will choose to spend their time and money at SLC (*followed by explanation of what it offers to customers*)
 - The **XP metaphor** technique explains a complex idea in simple, familiar terms, using common language and vocabulary
 - **Example:** SLC is the living room of Oasestown!



Help Everyone Understand the Vision



- **PRODUCT BOX EXERCISE:** A technique used to explain a desired solution or outcome. Stakeholders try to describe aspects of a solution in the same way a marketer might describe product features and benefits on a box.
- **XP METAPHOR:** A common Extreme Programming (XP) technique that describes a common vision of how a program works.

PRODUCT BOX EXERCISE:

A technique used to explain a desired solution or outcome.

Stakeholders try to describe aspects of a solution in the same way a marketer might describe product features and benefits on a box.



Example: E-learning Platform

- **Front of the Box:**
 - Name: "LearnHub."
 - Slogan: "Your Learning, Your Way."
 - Image of a laptop with students taking an online course.
- **Key Features:**
 - Wide range of courses (tech, business, arts).
 - Interactive quizzes and hands-on projects.
 - Certification upon completion.
 - Personalized learning paths.
 - Mobile-friendly for on-the-go learning.
- **Back of the Box:**
 - Benefits: "Upgrade your skills, enhance your career, learn at your pace."
 - Quote: "Education made easy and accessible to everyone."
 - Testimonials: "Flexible, affordable, and engaging."

XP METAPHOR: A common Extreme Programming (XP) technique that describes a common vision of how a program works.



Example: "The Factory" Metaphor for a Manufacturing Pipeline System

- **Example:** A system that processes data in stages can be compared to a factory production line:
 - **Raw materials** represent the initial input data.
 - **Machines or workstations** along the assembly line are like different processing units in the system.
 - **Conveyor belts** symbolize the data flowing from one stage to another.
 - **Finished products** represent the final output after processing is complete.

Got Agreement on the Project Agreements?



*There is no single way to create a **project charter**, but every project needs to have one!*

Once stakeholders and team members have accepted and can begin to internalize the project vision and agreements, it's time to ensure the project charter is finalized.

- **If there is no formal project selection process in an organization, a project professional may draft the project charter and review it with the executive sponsor (and possibly key stakeholders) for approval and distribution.**



Project Charter*

A document issued by the project initiator/sponsor or project manager with executive/stakeholder approval that formally authorizes the existence of a project and provides the project manager with the authority to apply organizational resources to project activities.

What it does and why it's important:

- Authorizes project
- Enables project manager to apply resources to project work
- Defines rationale and business need
- Verifies alignment with strategic goals
- Keeps everyone focused on a clear project vision



Sometimes a statement of work can serve as project charter.

Project Charter Contents:

- The project charter will look different depending on your organization and the project context and how well-developed the ideas are. Most practitioners recommend a simple, one-page document. It includes:
 - The names of key players — the sponsor, the project manager, key stakeholders.
 - The project description, including preliminary requirements and metrics.
 - Business needs, including financial goals.
 - A summary schedule and milestones.
 - Assumptions, boundaries and constraints, including overall project risk, project approval requirements and the approved budget.
 - The business case, including success and exit criteria.
- Assigned Project manager, responsibility, and authority level.
- Name and authority of the sponsor or another person (s) authorizing the project charter.

Shawpe Lifestyle Centre Project Charter: Activity

Timeline – 36 months

- **Phase 1** (12 months): Complete construction of interior spaces; recruit potential tenants
- **Phase 2** (24 months): Complete exterior construction; begin interior site occupancy with identified tenants
- **Phase 3** (from 30 months): Transfer property management to Oasestown partnership

Budget/financing

- Phase 1 capitalization of US \$7 million secured
- \$3 million annual revenue from rental income needed in Phase 2 to finance Phase 3

Vision

- Revitalize Oasestown
- Form community partnership with Oasestown
- Flagship project before regional expansion

Known challenges

- Site in historical conservation zone
- New vendors (glasswork and masonry)
- Physical retail market instability
- Resistant key stakeholder (Josie!)
- Phase 3 financing???

ECO Coverage

1.2 Lead a team

- Set a clear vision and mission (1.2.1)

1.8 Negotiate project agreements

- Analyze the bounds of the negotiation for agreement (1.8.1)
- Assess priorities and determine ultimate objective(s) (1.8.2)
- Participate in agreement negotiations (1.8.4)
- Determine a negotiation strategy (1.8.5)

1.10 Build shared understanding

- Survey all necessary parties to reach consensus (1.10.2)
- Support outcome of parties' agreement (1.10.3)

1.12 Define team ground rules

- Communicate organizational principles with team and external stakeholders (1.12.1)
- Establish an environment that fosters adherence to ground rules (1.12.2)

